

TECHNICAL REPORT (PART B)**COVER PAGE**

Part B of the Technical Report must be downloaded from the Portal Technical Report (Part B)/Termination Report screen, completed and then assembled and re-uploaded as PDF on that screen.

PROJECT	
Project number:	101101078-LIFE21-CAP-PL-CBP 4 LIFE_PL
Project name:	Capacity Building of LIFE NCP in Poland
Project acronym:	CBP 4 LIFE_PL

REPORTING PERIOD	
⚠ Please note that you must report on the entire reporting period.	
RP number:	Final
Duration:	from 01/02/2023 to 31/01/2026

TABLE OF CONTENTS

TECHNICAL REPORT (PART B)	1
COVER PAGE	1
1. OVERVIEW OF THE PROGRESS	2
1.1 Summary of work performed and achievements, results and impacts	2
2. IMPACT	6
2.1 Expected impacts	6
2.2 Sustainability, replication and exploitation	9
2.3 Complementary measures	10
3. IMPLEMENTATION	12
3.1 Work packages, activities, resources and timing	12
Work Package 1	12
Work Package 2	Błąd! Nie zdefiniowano zakładki.
Timetable	40
3.2 Impact monitoring and reporting	42
3.3 Communication, dissemination and visibility	42
4. RESOURCES	49
4.1 Consortium set-up	49
4.2 Project management	49
4.3 Budget	50
4.4 Risk management	50
4.5 Next phase: Changes/adjustments	51
5. FOLLOW-UP TO EU RECOMMENDATIONS	51
5.1 Follow-up to EU recommendations	51
6. OTHER	51
6.1 Ethics	51
6.2 Security	51
7. DECLARATIONS	52

#@PER-REP-LIFE@#

#@PRO-GRE-PG@# [This document is tagged. Do not delete the tags; they are needed for the processing.]

1. OVERVIEW OF THE PROGRESS

1.1 Summary of work performed and achievements, results and impacts

[OPTION 1 by default (all except OG):

Work performed and main achievements

Short summary of progress towards the project objectives. Highlight significant activities and achievements. Provide clear and measurable details.

Analyse the outcome of the project (so far) and its (actual and expected) impact (on target groups, change, innovation etc.). For the Final Report, include the conclusions of the action.

Report on objectives not fully achieved or not on schedule, as well as important problems and difficulties encountered during project implementation.

Summarise in one or two paragraphs important lessons learnt, critical observations on laws, regulations and/or policies that you would like to feedback to the policy directorates of the European Commission.

For SIPs/SNAPs: Specify in particular:

- Significant achievements in changing and influencing environmental, climate, social or economic policies.
- Other policies or plans (than those specifically targeted by the project) at a local, regional, national and/or EU/international level that have been supported through project activities.
- Legal or policy bottlenecks preventing the implementation of this or other relevant projects and/or the targeted plan/strategy/action plan.
- Lessons learnt or critical observations on changes needed to further the climate and environmental agenda in the Member State(s) or the EU.

 Do not simply cut and paste the project summary (filled in online on the Summary for Publication screen). Contrary to the summary, this section is for reporting to the EU and will not be published.

All project activities have been completed (including the modifications to certain actions proposed by CINEA and subsequently approved), all Milestones have been achieved, and all Deliverables have been submitted.

The outcomes of the first calls for proposals influenced by the project activities—namely the 2023 and 2024 calls—are excellent. Both KPI indicators have been significantly exceeded, reaching **175% and 258% of their respective target values**.

More information is provided in the section: [Expected impacts](#)

Activities carried out and main project achievements* in the period 1 February 2023 – 31 January 2026:

[WP1 \(T.1.1 - T.1.3\)](#) Establishment of the project team, continuous monitoring of implementation and achieved results (2023–2026) – completed in accordance with the plan.

[WP2 \(T.2.1 – T.2.5\)](#) The main objectives of WP2 were: improving the quality of applications, resulting in a higher number of accepted LIFE projects / expanding the Polish NCP's training offer by 15 dedicated training events for potential applicants, with approximately 700 participants / introducing a new, more accessible form of knowledge transfer – podcasts.

These objectives have been achieved, and in some cases the results have even exceeded the planned numerical targets (see – [Expected impacts](#)) / Under the project activities, **19 dedicated training events for potential applicants were delivered, involving nearly 1,200 participants**.

Scope of WP2 activities:

- T.2.1: The study “*Analysis of the Most Promising LIFE Themes in Poland*” (2024) was completed. With CINEA’s approval, the number of studies was reduced from two to one – see the T.2.1 description for further details. The analysis is used to complement and sectorally orient the Polish NCP’s existing information activities aimed at reaching entities with the greatest potential to implement LIFE projects.
- T.2.2: Nine thematic training sessions for applicants were delivered (2023–2025), as planned. Recordings are available on the [YouTube NFOŚiGW](#) – LIFE 2025 and LIFE 2023–2024 sections (a total of 924 participants / 1,187 YouTube views / 36h34’ of material available on YouTube).
- T.2.3: Ten application-preparation workshops were delivered (2023–2025), exceeding the six originally planned, including:
 - Four online workshops (2023), with recordings available on the [YouTube NFOŚiGW](#) – LIFE 2023–2024 section (a total of 179 participants / 1,654 YouTube views / 13h48’ of material available on YouTube);
 - Six in-person practical workshops (2024 and 2025) with a total of 87 participants.
- T.2.4: Ten podcasts from the “*LIFE: Short overview*” series were produced (2025), in line with the ten planned. Recordings are available on the [YouTube NFOŚiGW/podcasty](#) channel – 2,612 views in total – and on the Polish NCP website.
- T.2.5: Three training courses were delivered for the Polish NCP Team (2023–2025), as planned. These enabled NCP staff to acquire substantive knowledge and practical guidance relevant to training activities. The completed courses were: “*Professional Delivery of Training*” (2023) / “*Professional Delivery of Workshops on Developing the Logical Framework Matrix for LIFE Applications to the European Commission*” (2024) / “*Planning a LIFE Project According to the Project Cycle Management (PCM) Methodology*” (2025).

WP3 (T.3.1 – T.3.6) The main objectives of WP3 were: organising a minimum of six information-training events based on cooperation with networks of EU funds and programme information points, with approximately 750 participants in total / delivering three LIFE Information Days aimed at presenting examples of projects implemented in Poland and across Europe, involving approximately 1,000 participants / preparing a tool facilitating a rapid overview of key LIFE requirements and an initial verification of project concepts. The objectives have been achieved, and in some cases the results have exceeded the planned numerical values. **Six information-training events** (T.3.2 and T.3.4) were delivered, with over **2,100 participants**. The number of participants in the LIFE Information Days (T.3.3) **exceeded 2,700**.

Scope of WP3 activities:

- T.3.1: All planned media activities were completed, including:
 - Development of the project’s visual identity, which is used in the ongoing activities of the NCP LIFE in Poland;
 - Two advertising campaigns in each year of project implementation (2023–2025), in line with the planned 3×2 schedule, targeting individuals and institutions interested in environmental protection. The campaigns promoted the LIFE Programme and NCP LIFE in Poland. They were delivered in two annual blocks in the form of online display advertising (internet banner placement on selected websites redirecting users to the NCP LIFE in Poland [NCP LIFE in Poland](#) webpage). In total, 3,205,360 advertisement impressions and 18,185 clicks were achieved;
 - Five promotional films (2025) were produced, as planned. They were published on the YouTube channel (1,481 views in total) and are available on the Polish

- NCP website under the section [Programme LIFE – Why is it worth applying? – Films](#). In addition, five short film trailers were produced for use on social media to promote events related to the LIFE Programme;
- Preparation of ten articles (2023–2025), exceeding the nine planned. The articles were published across seven portals – nationwide, local-government and sector-specific (environmental and construction) – with a total of 75,439 views. The articles are available on the NCP LIFE in Poland website under [Press Articles – Polish NCP LIFE](#).
- T.3.2: Three online conferences “*Financing Environmental Protection from EU Programmes*” were organised (2023, 2024, 2025), as planned. Recordings are available on the NFOŚiGW YouTube channel (1,797 participants / 1,850 YouTube views / 9 hours of material available on YouTube).
 - T.3.3: Three two-day LIFE Information Days were organised (2023, 2024, 2025), as planned (3×2). Recordings are available on the NFOŚiGW YouTube channel. Participation reached: 764 in-person attendees / 1,985 online attendees / 2,586 YouTube views / 12 hours of material available on YouTube.
 - T.3.4: Three online training sessions for the European Funds Information Points were delivered (2023, 2024, 2025), as planned (329 participants / 704 YouTube views / 2h16’ of material available on YouTube).
 - T.3.5: The *YouTube LIFE PL Channel Navigator* was launched (2024). The *Online LIFE Program Navigator* was revised and completed as the *YouTube LIFE PL channel navigator* and is available on the website [Nawigator po kanale YouTube LIFE PL](#). The tool describes and facilitates navigation through almost 165 hours of training material delivered by NCP LIFE in Poland, covering various aspects of the LIFE Programme, produced over two LIFE Capacity Building Projects – CBP1 (2021–2022): 87 hours and CBP2 (2023–2026): 78 hours.
 - T.3.6: All planned information and promotional materials were prepared, including:
 - The publication “*Polish LIFE Projects*” was prepared and published, as planned, in PDF format on the [NCP LIFE in Poland](#) website, and as a printed edition (1,000 copies). Information about the PDF version was sent to 8,476 recipients (LIFE databases, LIFE newsletter, NFOŚiGW newsletter). A total of 255 printed copies were distributed to institutions cooperating in the promotion of the LIFE Programme – further distribution is described under T.3.6.
 - Information materials (brochure, 4,000 copies, as planned) and promotional materials (roll-ups, gadgets, as planned) were prepared and used on an ongoing basis for project purposes (2023, 2024, 2025).

WP4 (T.4.1 – T.4.3) The main objectives of WP4 were: increasing the participation of Polish entities in international projects successfully obtaining funding (by an average of 50% compared to the 2018–2020 baseline average of 4.33 projects) / publishing 20 cooperation offers / participating in approximately 25 individual brokerage/consultation meetings per year. The objectives have been achieved, and in several cases the results have exceeded the planned target values: **the average number of international LIFE projects approved by the European Commission in which Polish applicants participated as partners in the 2023 and 2024 calls reached 15.5 / 26 cooperation offers were published / Polish NCP staff participated in over 120 meetings with potential LIFE Programme applicants.**

Scope of WP4 activities:

- T.4.1: A database of potential applicants (448 entities) was developed, as planned, based on the “*Analysis of the Most Promising LIFE Themes in Poland*” (T.2.1). All entities in the

database were contacted in order to present the LIFE Programme offer, provide application consultations, support partner matching for LIFE projects, and inform them about the launch of calls, webinars and newly published LIFE-related materials.

- T.4.2: The Partner Search and Virtual 1:1 Meetings tools were promoted during events and webinars, as well as on the NCP LIFE in Poland website under: [Where to find partners for a LIFE project?](#). In addition, the NCP LIFE in Poland identified and verified cooperation offers available on the F&T portal in each published call under *Partner search announcements*, and selected offers (26 in total) were published on the Polish NCP website under [Find a project partner](#). These offers were also communicated to subscribers of the NCP LIFE in Poland Newsletter and to selected entities in Poland, including those from the Database of Potential Applicants (T.4.1), and promoted on the NCP LIFE in Poland LinkedIn profile. The Beneficiary decided to expand the scope of this task to include cooperation with *State Water Management Polish Waters (Państwowe Gospodarstwo Wodne Wody Polskie, PGW WP)* as a strategic partner (with CINEA's approval – see T.4.2 for more details).
- T.4.3: The Polish NCP promoted brokerage meetings – Virtual 1:1 Meetings – through multiple channels, including during events organised by the Polish NCP or events in which it participated, via the newsletter, and through information published on the Polish NCP website:
 - [Support for applicants in brokerage meetings organised by the European Commission – Virtual Meetings 1:1](#)
 - [Where to find partners for a LIFE project?](#)

Furthermore, the Polish NCP held more than 120 consultation meetings with potential applicants.

A total of **6,065 individuals/entities** participated in the **31 events** (information days, conferences, webinars, training sessions) organised under the project. Recordings of these events, as well as the produced podcasts and films, amount to **nearly 78 hours of training and informational material**, available on the [NFOŚiGW YouTube](#) channel in the LIFE 2025 and LIFE 2023–2024 sections, and have received **over 12,000 views** during the project period.

The following channels were used for information and promotional activities:

- The [NCP LIFE in Poland](#) website, which contains all information on the LIFE Programme and all materials developed under the CBP project, where 137 news updates were published (2023, 2024, 2025);
- The LIFE Newsletter, which reached 4,843 subscribers with 89 issues published (2023, 2024, 2025);
- The [NCP LIFE LinkedIn](#) profile, with 487 followers and 96 posts (2024, 2025).

Contractors were selected in accordance with the Polish Public Procurement Law and the NFOŚiGW Public Procurement Regulations (NFOŚiGW is a public entity obliged to apply the Public Procurement Law).

*The view statistics presented reflect the state as of 31 January 2026.

#\$PRO-GRE-PG\$# #@\$IMP-ACT-IA@#

]

[OPTION 2 for Operating Grants:

Work performed and main achievements

Short summary of progress towards the project objectives. Highlight significant activities and achievements. Provide clear and measurable details

Report on objectives not fully achieved or not on schedule (postponed to next year).

Analyse the outcome of the activities during the period covered by the EU grant and their impact (on target groups, change, innovation etc.), including a description of the European dimension and added value of the activities.

⚠ Do not simply cut and paste the project summary (filled in online on the Summary for Publication screen). Contrary to the summary, this section is for reporting to the EU and will not be published.

Insert text (max 5 pages)

#SPRO-GRE-PG\$# #@IMP-ACT-IA@#

]

2. IMPACT

2.1 Expected impacts

Impact

Report on changes to the expected impacts presented in your description of the action (DoA) (if any) and the effects on the project/need for adaptations.

Confirm that you have reported on the achieved key performance indicators (KPIs) in the [LIFE KPI webtool](#), in line with the agreed schedule. (n/a for Operating Grants, PRE, TA-PP, TA-R)

The results of the first calls for proposals influenced by the project activities – namely the 2023 and 2024 calls – are excellent.

Both KPI indicators were significantly exceeded, by 75% and 158% respectively.

a) Average number of LIFE projects approved by the European Commission:

Baseline value: 2.66 / Target value: 4

2023 calls: 8

101158113	LIFE23-CCA-PL-LIFE DREAM CITIES
101158336	LIFE23-CCM-PL-LIFeHDV
101167603	LIFE23-CET-FEPC
101167621	LIFE23-CET-LOCATEE
101155901	LIFE23-GIC-PL-LIFE ENSPIRE
101147995	LIFE23-NAT-PL-LIFEkulikPL
101147278	LIFE23-NAT-PL-LIFE for Dunes PL
101147291	LIFE23-SIP-PL-LIFE Pom GOZilla

2024 calls: 6

101198144	LIFE24-NAT-PL-Control IAS for LIFE
101212871	LIFE24-GIC-PL-LIFE OrgFluX-PL
101213071	LIFE24-NAT-PL-LIFE DRAWA BIS
101213967	LIFE24-CCA-PL-LIFE RIVEREASE
101216026	LIFE24-CET-LIFE-RenOSS-PL
101216284	LIFE24-NAT-PL-LIFE for RIVERS

Average value in the 2023 and 2024 calls: 7

In the 2023 and 2024 calls, this indicator reached **260% of the baseline value** and **175% of the target value**.

b) Average number of foreign LIFE projects approved by the European Commission in which Polish applicants participate as partners:

Baseline value: 4.33 / Target value: 6

2023 calls: 13

101158001	LIFE23-CCA-IT-LIFE CAPT-TILE
101167619	LIFE23-CET-BUSHROSSs (Ireland)
101167684	LIFE23-CET-CETAC (Czech Republic)
101167575	LIFE23-CET-DHC SwEEtch (Italy)
101167230	LIFE23-CET-ENERCOM FACILITY (Belgium)
101167597	LIFE23-CET-EPREL Services (Austria)
101167599	LIFE23-CET-ESCALATE (Germany)
101167644	LIFE23-CET-install.res (Austria)
101167717	LIFE23-CET-OCTOPUS (France)
101158058	LIFE23-GIC-BE-LIFE EFFECT
101148281	LIFE23-NAT-LT-LIFE4AquaticWarbler
101148740	LIFE23-PRE-FR-AGROWISE
101148077	LIFE23-PRE-IT-LIFE BE-WoodEN

2024 calls: 18

101212611	LIFE24-CCM-DE-LIFE SUPER EU
101212857	LIFE24-CET-BUSINESS2ACT
101213246	LIFE24-GIC-BE-Plan4Climate
101214286	LIFE24-TAE-DE-CARPATHIAN LIFE
101214736	LIFE24-ENV-BE-CEMLOOP XL
101215069	LIFE24-CET-I-EBRA
101215197	LIFE24-CET-BREEZE
101215402	LIFE24-CET-LIFE_PUBLINK
101215542	LIFE24-GIE-ES-LIFE CLEAN-AIR
101215621	LIFE24-CET-ENERGY POVERTY NEXUS
101215623	LIFE24-CET-SHINE
101215627	LIFE24-CET-LIFE EnerGISE
101215674	LIFE24-CET-ODYSSEE-MURE - EED
101215816	LIFE24-CET-EXQUISHEAT
101216157	LIFE24-NAT-CZ-LIFE Model Forest
101216180	LIFE24-ENV-SE-Ceilings4LIFE
101216229	LIFE24-PRE-UA-LIFE-U-SPRING
101250182	LIFE24-CET-EEFINH

Average value in the 2023 and 2024 calls: 15.5

In the 2023 and 2024 calls, this indicator reached **358% of the baseline value** and **258% of the target value**.

Contribution to the Plan/Strategy/Action plan (for SIPs/SNAPs) (max 7 pages)

Provide an overview of the achieved project's impacts (for the final report, : cover whole project duration).

Include an analysis of the project's contribution to/influence on the implementation of the targeted plan/strategy/action plan. Use figures, diagrams, etc. as relevant to help present your results.

Describe both quantitative and qualitative impacts such as environmental, economic and social impacts, contribution to policy development and implementation, innovations (related to technology, processes, methods and tools) and capacity building.

Briefly describe important barriers and recommendation for future work. Highlight any regional, national or European legislation that might have an impact on the implementation of your project.

Refer to deliverables that provide a full description, analysis and evaluation of your project's impacts.

Environmental benefits (direct / quantified) (for SIPs/SNAPs)

Describe the extent to which the targeted plan/strategy/action plan has been implemented and further developed. Describe any direct / quantitative environmental benefits, which may for example include:

for Environment SIPs:

- improvements in water quality; reductions of emissions, energy or resource savings
- quantified areas of known improvements (e.g. no. of properties/sites/water courses/other locations positively benefiting etc.)
- number of relevant barriers addressed

for Climate Action SIPs:

- reductions of greenhouse gas emissions
- increase of climate resilience, etc

for SNAPs:

- conservation benefits for Natura 2000 (SCI/SPA) and species/habitat types targeted
- also address incentive/pump priming effects (both in financial and policy terms)

Insert text

Environmental benefits (qualitative) (for SIPs/SNAPs)

Consider if there are any qualitative, or yet unquantified environmental impacts. As a minimum, address the following questions, and add any further discussion on qualitative impacts as necessary (note the last point concerns all SIPs/SNAPs):

Environment SIPs:

- Have there been any developments in long-term sustainable technology, from product to functional focus, from end-of-pipe to prevention?
- Is there a higher visibility and/or engagement and participation for environmental problems and/or solutions, with regulators, decision makers, interest groups and/or other stakeholders including the general public?
- Have there been any demonstrable, behavioural, organisational or procedural changes in any stakeholder groups?
- Is there any 'spin-off' or catalyst effects in other environmental themes and focus areas such as spatial and development planning, agriculture, forestry, or industry etc.

Climate Action SIPs:

- Have there been any developments in long-term sustainable technology? Report highlights related to better planning; change of behaviour; spin-off effect in other sectors (e.g. environment, industry, agriculture) etc.

SNAPs:

- Did the project eliminate the threats defined in Annex 1 of the Grant Agreement? What are the remaining/new threats? Details should be given regarding what actions should be carried out, when, by whom and using what sources of finance?
- How will the project enable the project partners and stakeholders to fully implement the PAF and related plans?

All SIPs/SNAPs — multi-benefit approach:

- A SIP/SNAP should, as far as possible, deliver benefits in several other policy areas beyond the core target of the project and the targeted plan/strategy/action plan, such as contributing to the integration of the environment and climate policies into other policies and/or if it contributes to sustainable development.
- Indicate if it created synergies with the objectives of other EU policies in particular those that can be targeted by/subject of SIP/SNAP.

Insert text

Economic and social benefits (for SIPs/SNAPs)

Economic benefits may include discussion on cost savings and/or business opportunities such as those with new processes or technologies etc. It could also include regional development and cost reductions or revenues in other

sectors. In particular, state the number of full time equivalent (FTE) jobs created and supported, showing a breakdown in qualified/non-qualified staff.

Social benefits may include any discussion on the positive effects resulting from the project activity on employment, health, ethnic integration, equality, and any other socio-economic impact etc.

Discuss whether these benefits are directly measured, predicted/modelled (and alternatively, if they are not measured but considered likely).

Insert text

Capacity building (for SIPs/SNAPs)

Describe the specific capacity building activities that were implemented in the reporting period by the project with the aim of the full implementation of the targeted plan/strategy/action plan.

Describe as well capacity building, upskilling, training, and organisational and administrative changes that result in increased capacity for the beneficiaries, or stakeholders including the general public, but that are not directly related to the implementation of the plan/strategy/action plan.

Insert text

Policy implications (for SIPs/SNAPs)

Describe any important contribution to the future implementation, design or take-up of regional, national or European legislation related to the targeted plan/strategy/action plan and its further implementation and development.

Highlight any potential unintended impacts, bottlenecks or barriers to the implementation of your project due to regional, national or European legislation including recommended actions further to actions already taken to overcome these barriers.

Also describe any further, unforeseen items of local/regional, national, or international policy that are being supported or influenced by the project, which were not foreseen in the original project. Describe how these are being supported and/or influenced.

Insert text

#@S

US-CON-SC@#

2.2 Sustainability, replication and exploitation

Sustainability, replication and exploitation (n/a for Operating Grants)

Report on changes in your sustainability analysis/strategy (if any).

Briefly describe the key results of your project that will have a long-lasting effect, or will be replicated or exploited. Highlight those sectors or places with the highest potential for replicating the project's results. Highlight any public or private actors likely to up-scale the project's results and estimate the required investments or financial resources (if any) that would be necessary to up-scale. Describe the coverage and size of the target market.

For the Final Report, describe the follow-up of the project after the end of the EU grant. How will the results be used or further developed. Report on the status and content of your [After LIFE conservation plan] [Business plan] [Exploitation plan] to ensure sustainability of results and long-term impact.

For SIPs/SNAPs:

Describe briefly how you will ensure the continued implementation of the targeted plan/strategy/action plan after the end of the LIFE funding, covering the following (for interim report only cover aspects not reported before or if there have been substantial changes with respect to previous reports):

- the mechanisms that are or will be put in place to facilitate the continued implementation
- the tasks/work packages that will have to be carried out or continued and their timeframe
- the level of resources (in terms of staffing and budgets compared to levels during the project) required
- securing the necessary financing (cover both the LIFE actions and, if possible and relevant, the complementary actions in this discussion)
- maintaining and expanding the human and technical capacities built up during the project. Estimate the likelihood that staff recruited and/or trained during the project will continue to be actively involved. Identify the members of the project team that will continue to be involved
- the main pieces of equipment purchased under the project and that beneficiaries continue to use and maintain for at least five years after the end of the action or until the end of their economic lifespan

– *the continuation of dissemination activities.*

The project does not include a formal sustainability strategy; however, its integration within the structures of the Polish NCP ensures that the most essential activities related to promoting the LIFE Programme will be maintained and continued in the future.

These include:

- Practical workshops on preparing LIFE applications, delivered on the basis of the model developed under the CBP2 project (T.2.3);
- Continued dissemination of podcasts (T.2.4), promotional films (T.3.1) and webinars (T.2.2);
- Ongoing use of the visual identity (T.3.1);
- LIFE Information Days (T.3.3);
- Continuous updating and promotion of the *YouTube LIFE PL Channel Navigator* (T.3.5);
- Ongoing use of information materials (brochure), promotional materials (roll-ups) and the publication *“Polish LIFE Projects”* (T.3.6);
- Maintaining regular contact with potential applicants from the LIFE Potential Applicants Database (T.4.1), providing support in preparing applications and in identifying partners for potential projects;
- Promotion of CINEA tools: *Partner Search* and *Virtual 1:1 Meetings* (T.4.2);
- Publishing cooperation offers received by the Polish NCP on the website;
- Ongoing meetings with potential applicants – consulting project ideas and discussing the composition of potential consortia (T.4.3).

These activities will continue until the last call of the current EC financial perspective. Due to uncertainty regarding the future of the LIFE Programme in the next financial perspective, it is anticipated that decisions concerning the further involvement of NFOŚiGW in the LIFE Programme will be taken in 2028.

#§SUS-CON-SC§#

2.3 Complementary measures

Implementation of the complementary measures *(for SIPs/SNAPs)*

If not included in a previous report, explain the coordination mechanisms established with other funds, to optimise the use of funds for the targeted plan/strategy/action plan (e.g. to properly allocate funding to key priorities, etc.). Also describe (if applicable) how the mechanisms for attracting additional funding created benefits for stakeholders.

If already previously reported, focus only on main new progress/achievements of the coordination and fund mobilisation (as compared to the previous reports).

Describe the results of the complementary measures and actions following the structure defined in Annex 1 of the Grant Agreement or using the pillar/theme approach agreed with the granting authority. Describe successes, challenges, and mobilised resources.

Describe in qualitative and to the extent possible in quantitative terms the overall progress with the implementation of the targeted plan/strategy/action plan resulting from the complementary measures and actions. Cover at least: (i) environmental benefits, (ii) policy implications (if not already reported above), and (iii) capacity building and sustainability.

Describe any substantial changes to the complementary measures and actions and how this may affect the implementation of the targeted plan/strategy/action plan and the SIP/SNAP project.

Please also complete the table below for each complementary measure or action.

Final report: cover whole project duration.

Insert text

Name of complementary action	Source of funding	Estimated funding amount	Actual funding amounts to date	Contribution to targeted Plan/Strategy/Action plan <i>How did the SIP/SNAP project work with the complementary measure or action (e.g.</i>
------------------------------	-------------------	--------------------------	--------------------------------	---

		<i>as per proposal application</i>	<i>committed (C), mobilised (M) and/or spent (S)</i>	<i>regular phone calls, joint project or conference, common paper, etc.)?</i> <i>Which SIP/SNAP work packages or tasks are linked? Provide references, web links to reports, dates and other relevant information. Highlight how the SIP/SNAP project facilitated the implementation of the complementary measure or action.</i>
Insert text	Insert text	EUR XXX million	[EUR XXX million (C)]	Insert text

#§IMP-ACT-IA§#

#@WRK-PLA-WP@#

3. IMPLEMENTATION

3.1 Work packages, activities, resources and timing

WORK PACKAGES

Work Package 1

Work Package 1: Project management & coordination

Activities

Explain the work carried out for each work package during the reporting period, giving details of the work carried out by each participant involved. Please summarise in a few sentences what was done in the previous period, when applicable.

Explain the reasons for deviations from Annex 1 of the Grant Agreement, the consequences and the proposed corrective actions.

Include explanations for tasks not fully implemented, critical objectives not fully achieved and/or not being on schedule. Explain also the impact on other tasks, on the available resources and the planning. Where necessary, make reference to the deliverables in the report text. In case of major deviations from on the planned budget, please refer to section 4.3.

*Focus only on the **main results** as well as important **lessons learned**. The technical details should be provided in the deliverables.*

Additionally, for Operating Grants, report under Work Package 1 on changes in your organisation's capacity (if any) to become a more efficient stakeholder in the EU's policy process. Report on the proposed actions and their status to develop the organisation, widen the grassroots or members base, diversify and sustain the organisation's fundraising strategy and the strategy to reduce your dependence on LIFE operating grants.

T.1.1. Establishment of the project team [Implemented]

Following the calculation of working time, it was determined that the actual time worked amounted to 85.81% of the planned involvement (78.95 / 92 person-months).

The project team was established as of **1 February 2023**, composed of NFOŚiGW employees, by modifying their job descriptions.
(...)

T.1.2 Monitoring of project implementation [Implemented 100%]

In **February 2023**, meetings were held with the organisational units of NFOŚiGW involved in the implementation of the project – the **Promotion Department, Accounting, Human Resources and Public Procurement** – to establish the principles of cooperation. Between **October and November 2023**, a review was carried out of the status of project implementation, the materials produced, preparations for subsequent stages, and proposed changes to the activities and materials planned for delivery. The procedure for selecting the contractor for the *“Analysis of the Most Promising LIFE Themes in Poland”* was launched.

On **15 November 2023**, a **visit by the Project Monitor** took place – an audit of the implementation status, documentation (including HR and financial documentation), archiving procedures, and discussion of plans and proposed changes – with no significant comments from the Monitor.

In **January 2024**, further meetings were organised with the NFOŚiGW organisational units involved in the project – **the Promotion Department, Accounting, Human Resources and Public Procurement** – summarising cooperation to date and informing them of the outcomes of the CINEA project monitoring and the monitor’s recommendations. A review of project implementation was carried out. The 2024 events plan was prepared, together with an assessment of readiness for further implementation, budget status and proposed implementation changes. A needs assessment for additional resources was conducted and a plan to recruit additional staff was drafted. In the first quarter of 2024, conceptual work continued on podcasts, films, articles, webinars, conferences and LIFE Information Days. (...).

At the turn of April and May 2024, the main focus was placed on preparing the most demanding event – the LIFE Information Day, held on 14 and 16 May 2024. In the following months, (...) divided their duties within CBP2, including consultations on LIFE applications for the calls launched on 18 April 2024.

Matters related to the project were addressed during weekly meetings of the LIFE Department, with the Director of the organisational unit participating as required. When necessary, dedicated meetings concerning specific project activities were organised, including with representatives of other NFOŚiGW organisational units involved in the project: the Promotion Department, Accounting, Human Resources and Public Procurement.

Over the course of the project, five semi-annual reports were submitted to the supervisors of the Project Manager: for the first and second half of 2023; the first and second half of 2024; and the first half of 2025.

Milestones and deliverables were monitored on an ongoing basis, with the relevant sections of the Funding & Tenders portal being regularly updated.

T.1.3 Monitoring of achieved results [Implemented, at 175% and 258% respectively]

Under this task, the achievement of the project's output results was monitored on an ongoing basis, as described in section 1.1 of this form.

After the conclusion of the calls, an analysis was carried out to assess the impact of the project activities on the project indicators. The results of this analysis are presented in section 2.1 above.

In summary:

The results of the first calls influenced by the project activities – namely the 2023 and 2024 calls – are excellent. Both KPI indicators were significantly exceeded, by 75% and 158% respectively.

Indicator: **Average number of LIFE projects approved by the European Commission:**

In the 2023 and 2024 calls, this indicator reached 260% of the baseline value and 175% of the target value.

Indicator: **Average number of foreign LIFE projects approved by the European Commission in which Polish applicants participate as partners:**

In the 2023 and 2024 calls, this indicator reached 358% of the baseline value and 258% of the target value.

Other issues

Mention and explain unexpected events and adjustments that had to be made. Explain impact on other tasks, available resources and planning/timing. In case of major deviations from the planned budget, please refer to section 4.3.

Apart from the frequent staffing changes at the beginning of the project's implementation, no significant deviations from the assumptions of WP1 were identified. The composition of the project implementation team stabilized in April 2024.

Milestones and deliverables (outputs/outcomes)

See Technical Report (Part A).

Work Package 2

Work Package 2: Expansion and improvement of "LIFE Support"

Activities

Explain the work carried out for each work package during the reporting period, giving details of the work carried out by each participant involved. Please summarise in a few sentences what was done in the previous period, when applicable.

Explain the reasons for deviations from Annex 1 of the Grant Agreement, the consequences and the proposed corrective actions.

Include explanations for tasks not fully implemented, critical objectives not fully achieved and/or not being on schedule. Explain also the impact on other tasks, on the available resources and the planning. Where necessary, make reference to the deliverables in the report text. In case of major deviations from on the planned budget, please refer to section 4.3.

*Focus only on the **main results** as well as important **lessons learned**. The technical details should be provided in the deliverables.*

Additionally, for Operating Grants, report under Work Package 1 on changes in your organisation's capacity (if any) to become a more efficient stakeholder in the EU's policy process. Report on the proposed actions and their status to develop the organisation, widen the grassroots or members base, diversify and sustain the organisation's fundraising strategy and the strategy to reduce your dependence on LIFE operating grants.

T.2.1 Analysis of the Most Promising LIFE Themes in Poland [Implemented, at 50%*]

(...)

Conclusions from the Analysis:

- The study provides a valuable complement to the knowledge base of the Polish NCP, and the priority themes identified therein have been used to guide subsequent media and substantive activities, including within T.3.1.
- At the same time, the findings of the analysis largely coincide with the existing experience of the Polish NCP, gained through its ongoing work and through information obtained during the cyclical conference “*Financing Environmental Protection from EU Programmes*” organised under the CBP2 project (T.3.2).
- Furthermore, the most promising LIFE themes identified in the study—within the ENV and CLIMA areas, specifically in the context of Polish legal and financial conditions—are to a large extent niche, and their practical application is likely to remain limited.
- The list of the most promising entities from the perspective of applying for LIFE funding, provided as an annex to the Analysis, will be used under task T.4.1.
- The list includes numerous entities with which the Polish NCP already maintains contact (e.g. Agricultural Advisory Centres, ministries and universities).
- In view of the above, and due to the thematic overlap between the first and second Multiannual Work Programmes, it was concluded that there is no need to prepare the second analysis of the most promising LIFE themes in Poland originally foreseen in the project.

The results of the analysis were used in the implementation of tasks: T.3.1 (advertisements and articles), T.3.4 (training for European Funds Information Points, PIFE), and T.4.1 (database of potential LIFE applicants).

*Taking into account conclusion no. 6, the Polish NCP proposed in the mid-term report to reduce the originally planned scope of task T.2.1 (i.e. the preparation of Study No. 1 in 2023 and Study No. 2 in 2025), namely the cancellation of the second study planned in the

project and the use of the saved funds for underestimated tasks, such as adapting webinar recordings. CINEA approved the proposed change in its letter Ref. Ares(2025)577234 – 24/01/2025.

T.2.2 Thematic Training Sessions for Applicants (3 × 3) [Implemented, 100%]

A total of nine training sessions were organised (out of nine planned): one in 2023, two in 2024 and six in 2025.

All training sessions were delivered as online webinars.

The sessions were promoted via NFOŚiGW and LIFE social media channels, the LIFE Newsletter, the NFOŚiGW Newsletter, as well as through emails to the database of potential applicants developed under the “Analysis of the most promising LIFE themes in Poland” (T.2.1).

Speakers included, among others, representatives of the European Commission, beneficiaries of LIFE projects, and staff from the Polish NCP.

Recordings of the sessions are available on the [NFOŚiGW YouTube](#) channel, in the LIFE 2025 and LIFE 2023–2024 sections.

Totals: 924 participants / 1,187 YouTube views / nearly 74 hours of material on YouTube.

Training Sessions 2023:

- [LIFE in Business – Close2Market \(C2M\)](#) (16 March 2023), with the participation of representatives of the European Commission (118 participants / 493 YouTube views)

Training Sessions 2024:

- [LIFE for Water and Aquatic Ecosystems](#) (6 November 2024) (109 participants / 253 YouTube views)
- [Polish Co-beneficiaries of Foreign LIFE Projects](#) (4 December 2024) (28 participants / 246 YouTube views)

Training Sessions 2025:

- [Selected Polish LIFE Projects from the 2023 Call](#) (26 November 2025) (140 participants / 40 YouTube views)
- [Outcomes of Selected Polish Nature-related LIFE Projects](#) (5 December 2025) (145 participants / 52 YouTube views)
- [Tools for Proposal Preparation \(problem tree / objective tree / AI\)](#) (9 December 2025) (165 participants / 103 YouTube views)
- [Outcomes of Selected Polish Environmental LIFE Projects](#) (12 December 2025) (74 participants / 13 YouTube views)
- [Outcomes of Selected Polish LIFE Projects in the Field of Climate Protection](#) (16 December 2025) (84 participants / 23 YouTube views)
- [Outcomes of Selected Polish LIFE Projects in the Field of CET](#) (19 December 2025) (61 participants / 45 YouTube views)

T.2.3 Practical Workshops on Proposal Preparation Targeted at Specialists (3 × 2) [Implemented at 160%]

A total of ten workshops were organised (compared to six originally planned). The increased number resulted from needs identified by the Polish NCP among potential applicants.

2023 – Four Online Workshops (Two planned under the project + two additional ones replacing the two training sessions initially foreseen for 2023 as part of activity T.2.2, in accordance with the approval granted by the European Commission on 13 April 2023 via the F&T Communication Centre.)

- 11 May 2023 - [NATURE projects](#) (61 participants / 259 YouTube views)
- 17 May 2023 - [ENVIROMENT projects](#) (32 participants / 362 YouTube views)
- 25 May 2023 - [CLIMAT projects](#) (47 participants / 725 YouTube views)
- 30 May 2023 - [CET projects](#) (39 participants / 308 YouTube views)

Recordings of the workshops constitute training materials of the Polish NCP and are available on the [NFOŚiGW YouTube](#) channel.

Total: 179 participants / 1,654 YouTube views / nearly 14 hours of material on YouTube.

2024 - Two In-Person Practical Workshops on LIFE Proposal Preparation

- 20 June 2024: Nature protection projects (NAT sub-programme and CLIMA projects involving nature-related aspects) / 13 participants
- 21 June 2024: Environmental protection projects (ENV, CLIMA and CET sub-programmes) / 16 participants

Total: 29 participants.

2025 - Four In Person Practical Workshops on LIFE Proposal Preparation

- 14 January 2025: Nature protection projects (LIFE Nature and Biodiversity sub-programme, and CLIMA projects including nature-related aspects) / 18 participants
- 22 January 2025: Environmental protection projects (LIFE Circular Economy and Quality of Life; Climate Change Mitigation and Adaptation; Clean Energy Transition) / 12 participants
- 25 June 2025: Environmental protection projects (same sub-programmes as above) / 16 participants
- 26 June 2025: Nature protection projects (LIFE Nature and Biodiversity; and CLIMA projects with nature-related components) / 12 participants

Total: 58 participants.

T.2.4 Podcast Series on Key Aspects of Project Preparation (10) [Implemented, 100%]

Work on the concept for a series of ten podcasts commenced in January 2024. Each episode was intended to address a different topic related to the preparation of applications for the LIFE Programme or its sub-programmes. The thematic scope for all ten podcasts, as well as the graphic and production assumptions, were defined. Work began on the substantive content of the first five podcasts, prepared by the staff of the Polish NCP for LIFE. Due to staffing changes within the Department in April 2024, implementation was rescheduled for the period October 2024 – January 2025.

The podcasts were produced by a subcontractor selected in accordance with Polish Public Procurement Law, under a framework agreement concluded by NFOŚiGW. In October and November 2024, work was carried out on substantive preparation, including the development of conversation scripts and slides for five episodes. Recording sessions were held on 19 and 20 November 2024 with the participation of representatives of five LIFE projects, after which editing and corrections of the recordings commenced. All work on the preparation and production of the podcasts was completed on 24 January 2025.

The podcasts were ultimately released under the joint title “LIFE: Short overview”. Between 19 February and 23 April 2025, one podcast per week was published on the NFOŚiGW YouTube channel.

All episodes are available on the Polish NCP website under the section: [Video Podcasts “LIFE: Short overview”](#)

Podcast – publication date – view count:

1. [Introduction to the LIFE Programme](#) (19 February 2025) – 524 views
2. [LIFE Sub-programmes: Nature / Environment / Climate](#) (26 February 2025) – 296 views
3. [LIFE Clean Energy Transition Sub-programme](#) (5 March 2025) – 276 views (The National Energy Conservation Agency shared its experience as the coordinator of two LIFE CET projects and presented the benefits and challenges of the sub-programme, using the following projects as examples: [LIFE21-CET-BUILDSKILLS--BUPS-Poland/101076976](#) / [LIFE23-CET-FEPC/101167603](#))
4. [The Environmental Problem, Project Objectives and LIFE Project Results](#) (12 March 2025) – 228 views (PROZON Climate Protection Foundation shared its experience as the coordinator of three LIFE projects and discussed lessons learned from preparing LIFE proposals, based on: [LIFE18 CCM/PL/001100](#) / [LIFE22-GIC-PL-LEGAL-HFC-4-LIFE/101113459](#) / [LIFE22-ENV-PL-RE-ELECTRO-4-LIFE/101113652](#))
5. [Partnership in LIFE Projects](#) (19 March 2025) – 184 views (The Institute for Ecology of Industrial Areas (IETU) shared its experience as a partner in four LIFE projects and discussed the benefits and challenges of participation, based on: [LIFE08 ENV/IT/000399](#) / [LIFE19 GIE/PL/000784](#) / [LIFE20 GIE/FR/000282](#) / [LIFE21-ENV-PL-plasticLIFEcycle/101074161](#))
6. [Financial Support for Third Parties](#) (26 March 2025) – 299 views (Polish Society for the Protection of Nature “pro Natura” shared its experience in successfully using sub-grants in its project: [LIFE20 NAT/PL/001427](#))
7. [Volunteering](#) (2 April 2025) – 110 views (Karkonosze National Park and the Naturalists’ Club shared their experience in successfully implementing volunteering activities in the project: [LIFE20 NAT/PL/000151](#))
8. [Close to Market \(C2M\) Projects](#) (9 April 2025) – 138 views (MGGP Aero Sp. z o.o. shared its experience in implementing C2M activities within the project: [LIFE21-CCA-PL-LIFECOOLCITY/101074553](#))
9. [Financial Aspects](#) (16 April 2025) – 287 views
10. [The LIFE Programme Online](#) (23 April 2025) – 270 views

Summary: Across all ten podcasts, a total of 2,612 YouTube views were recorded, with nearly 3 hours and 41 minutes of content published on the NFOŚiGW YouTube channel.

The podcasts were promoted using NFOŚiGW/LIFE communication channels. Each episode was accompanied by:

- a news update on the NFOŚiGW / Polish NCP LIFE website
- a LinkedIn post by the Polish NCP LIFE
- a repost on LinkedIn by NFOŚiGW
- a Facebook post by NFOŚiGW
- inclusion in the Polish NCP LIFE Newsletter

Additionally, the podcasts were promoted during LIFE Info Days, applicant workshops, and consultation meetings.

T.2.5 Training and support for Polish NCP staff (3) [Implemented, 100%]

Three two-day training sessions were organised to strengthen the skills of Polish NCP staff in supporting applicants in preparing LIFE Programme proposals, as well as in delivering training sessions, workshops and presentations – both in person and online.

The training sessions were organised by an external contractor selected in accordance with the Polish Public Procurement Law.

5–6 June 2023: training course “Professional Delivery of Training”

The training aimed to enhance participants' competences in the professional preparation of presentations, techniques for generating interest in the subject matter and maintaining audience engagement, frameworks for developing training materials, clarity and optimisation of content delivery, WCAG requirements, selecting appropriate techniques for in-person sessions and webinars, as well as in designing and delivering webinars.

22–23 May 2024: training course “Professional Delivery of Workshops on Developing the Logical Framework Matrix for LIFE Applicants to the European Commission”

The objective of the training was to strengthen participants' competences in delivering training sessions, to structure their knowledge of the trainer's role, the training process and the management of challenging situations. The training focused on practical tools for facilitating workshops, as well as on developing the project Logical Framework Matrix and conducting stakeholder analysis based on it.

20–21 March 2025: training course “Planning a LIFE Project According to the Project Cycle Management (PCM) Methodology”

The training aimed to enhance participants' competences in effective planning and management of LIFE projects in accordance with the PCM methodology – to organise and/or expand their knowledge regarding project preparation and implementation, enabling LIFE NCP staff to share this expertise with LIFE applicants and thereby support them during project design and application development for the LIFE Programme.

Other issues <i>Mention and explain unexpected events and adjustments that had to be made. Explain impact on other tasks, available resources and planning/timing. In case of major deviations from the planned budget, please refer to section 4.3.</i>	T.2.1 With CINEA's approval, the second planned study "<i>Analysis of the Most Promising LIFE Themes in Poland</i>" was cancelled. T.2.2 With CINEA's approval, the training schedule was modified and additional sessions were delivered in the fourth quarter of 2025. Two training sessions originally planned for 2023, together with the practical workshops under task T.2.3, were conducted as four online workshops. T.2.3 With CINEA's approval, the number of workshops was increased from the planned 6 to 10. T.2.5 With CINEA's approval, the training dates were modified. The sessions originally planned for 2023 and 2024 were rescheduled.
Milestones and deliverables (outputs/outcomes)	
See Technical Report (Part A).	

Work Package 3

Work Package 3: Dissemination of information on the LIFE Programme
Activities <i>Explain the work carried out for each work package during the reporting period, giving details of the work carried out by each participant involved. Please summarise in a few sentences what was done in the previous period, when applicable.</i> <i>Explain the reasons for <u>deviations</u> from Annex 1 of the Grant Agreement, the consequences and the proposed corrective actions.</i> <i>Include explanations for tasks not fully implemented, critical objectives not fully achieved and/or not being on schedule. Explain also the impact on other tasks, on the available resources and the planning. Where necessary, make reference to the deliverables in the report text. In case of major deviations from on the planned budget, please refer to section 4.3.</i> <i>Focus only on the main results as well as important lessons learned. The technical details should be provided in the deliverables.</i> <i>Additionally, for Operating Grants, report under Work Package 1 on <u>changes</u> in your organisation's capacity (if any) to become a more efficient stakeholder in the EU's policy process. Report on the proposed actions and their status to develop the organisation, widen the grassroots or members base, diversify and sustain the organisation's fundraising strategy and the strategy to reduce your dependence on LIFE operating grants.</i>

T.3.1. Media activities

a) Development of the project's visual identity [Implemented, 100%]

A visual identity system for the project – the *NCP LIFE in Poland Brand Book* – was prepared.

Due to ongoing work on updating the NFOŚiGW logo and Brand Book, the work on the NCP LIFE in Poland logo and Brand Book was postponed; therefore, the full set of materials was finalised in October 2023.

The materials produced have been used during events and promotional meetings.



b) Series of press and online advertisements on LIFE (3 × 2) [Implemented, 100%]

In each year of the project (2023 / 2024 / 2025), advertising campaigns were carried out promoting the LIFE Programme and the Polish NCP in the form of online display advertising, i.e. through the publication of internet banners on selected websites that redirected users to the [NCP LIFE in Poland](#) webpage. Each campaign consisted of two series of advertisements per year, resulting in six series in total, in line with the plan.

The campaigns targeted individuals and institutions interested in various aspects of environmental protection. The selection of websites, advertising formats and implementation was carried out in cooperation with Media Houses working with NFOŚiGW under a framework agreement concluded in accordance with the Polish Public Procurement Law.

The advertising activities planned for 2024 and 2025 were developed on the basis of the conclusions drawn from the 2023 campaign and from the “Analysis of the Most Promising LIFE Themes in Poland” (T.2.1). Target groups were further specified as follows:

- Individuals with a general interest in environmental protection, in order to continuously expand the applicant base and promote the LIFE Programme;
- Specialists representing the business sector, NGOs, sustainable architecture, as well as developers and engineers.

Details of individual advertising campaigns:

2023:

24–30 June (series 1) on one portal: Wirtualna Polska / Money.pl, and 26–29 June (series 2) on one portal: Egospodarka.pl – totalling 685,579 impressions and 2,643 clicks.



**Sięgnij po dotacje
z programu LIFE**

Advertising banners were published on the portals, and clicking on the banners redirected users to the main advertisement published on the NFOŚiGW/LIFE website.

Effectiveness of the advertisements:

Money.pl – 670,000 impressions, 2,612 clicks (redirects to the [NCP LIFE in Poland](#) website),

Egospodarka.pl – 16,000 impressions, 31 clicks.

2024:

14–20 October (series 1) and 11–17 November (series 2) – 823,000 impressions and 863 clicks.



The activities targeted individuals and institutions interested in broadly understood environmental protection and ecological construction. The objectives of the campaign were defined as follows:

- Supporting the implementation of EU environmental law;
- Promoting the LIFE Programme and the co-financing of LIFE projects by NFOŚiGW;
- Encouraging potential beneficiaries to familiarise themselves with the LIFE Programme offer and available forms of funding;
- Reaching a precisely defined target group, including individuals interested in environmental protection and ecological construction, architects, designers, urban planners, developers, engineers, NGOs, representatives of national and regional public administration, as well as entrepreneurs and users of industry-specific portals.

The media plan was developed by the Media House and covered 35 specialised portals.

During 14–20 October 2024, the campaign generated 400,668 impressions and 445 clicks, reaching 140,201 users.

During 11–17 November 2024, the campaign generated 422,371 impressions and 418 clicks, reaching 202,481 users.

2025:

2–15 June (series 1) and 23–29 June (series 2) – 1,697,360 impressions and 15,155 clicks.



The activities targeted individuals and institutions interested in the broad field of environmental protection.

The objectives of the campaign were defined based on previous experience:

- Supporting the implementation of EU environmental law;
- Promoting the LIFE Programme and the funding opportunities offered by NFOŚiGW;
- Attracting the interest of potential beneficiaries in the LIFE Programme offer and encouraging them to apply for funding;
- Reaching specific target groups, including environmental protection specialists, designers and architects, engineers and developers, representatives of public administration and institutions, NGOs, entrepreneurs and users of industry-specific portals.

The revised assumptions regarding the timing of advertisement publication contributed to improved campaign results and more effective outreach to a broad and diverse audience.

The media selection designed by the Media House covered 61 portals, targeting various groups of recipients: Business: 20 portals, Local Government: 10 portals, NGOs: 2 portals, Environment: 10 portals, Construction / Architecture: 12 portals, Engineering: 7 portals

The advertising campaigns contributed to increased recognition of the LIFE Programme and enhanced awareness of available funding opportunities. In total, 3,205,360 advertisement impressions and 18,185 clicks were achieved.

c) Series of short promotional films / animations (5) [Implemented, 100%]

Concept: Common title: *“LIFE Programme – Why is it worth it?”*

Each film is 3–4 minutes long, with a shared opening sequence and closing slides. The films present the four LIFE Sub-programmes through short informational slides and highlight their benefits and advantages through statements from Polish LIFE Beneficiaries, illustrated with relevant visual material based on projects implemented in Poland. The films are available on the NFOŚiGW/LIFE YouTube channel.

On 16 May 2024, during the LIFE Information Days, recordings were made of statements from five LIFE Beneficiaries representing different types of entities eligible for LIFE funding: a national park, a commercial company, a local government unit, a research institute and a public institution.

2Q2024–3Q2024:

- Preparation of film scripts, narration texts and graphic materials relating to Polish LIFE projects;
- Contractor selection procedure for the editing, production and WCAG-compliant adaptation of the five films, carried out in cooperation with the Department of Promotion and Communication.

4Q2024 – Implementation:

- The films also used video and photographic materials provided by LIFE Beneficiaries, with whom appropriate copyright licensing agreements had been concluded;
- In addition to the five full-length films, five shortened versions (trailers) were produced under the contract for use in promoting the films on the Polish NCP and NFOŚiGW social media channels.

The films were produced by an external contractor selected in accordance with the Polish Public Procurement Law.

Publication and promotion of the films began on 8 January 2025 and continued until 5 February 2025.

The films were published weekly on the [NFOŚiGW YouTube channel / podcasts section](#), and are also available on the Polish NCP website in the dedicated section: [LIFE Programme – Why is it worth it? – Films](#)

(Title – publication date – number of views):

- [LIFE – Nature and Biodiversity – illustrated by a project implemented by a national park](#) – 8 January 2025 – 341 views
- [LIFE – Circular Economy and Quality of Life – illustrated by a project implemented by a commercial company](#) – 15 January 2025 – 329 views
- [LIFE – Climate Change Mitigation and Adaptation – illustrated by a project implemented by a local government unit](#) – 5 February 2025 – 330 views
- [LIFE – Climate Change Mitigation and Adaptation – illustrated by a project implemented by a research institute](#) – 29 January 2025 – 184 views
- [LIFE – Clean Energy Transition – illustrated by a project implemented by a public entity \(operating under commercial law\)](#) – 22 January 2025 – 297 views



The films were promoted using NFOŚiGW/LIFE communication channels. Each time, the promotion included:

- a news item on the NFOŚiGW / LIFE NCP website;
- a post on the LIFE NCP LinkedIn profile;

- a repost on the NFOŚiGW LinkedIn profile;
- a post on the NFOŚiGW Facebook page;
- the LIFE NCP newsletter.

In addition, the films were used during LIFE Information Days, workshops for applicants and consultation meetings, as well as for communicating upcoming LIFE Programme call deadlines announced by the European Commission. The films are available on the NFOŚiGW/LIFE YouTube channel.

In total, as of 31 January 2026, the films had been viewed 1,481 times.

d) Series of articles in the press or other specialised media (3 × 3) [Implemented, 111%]

Over the three-year period, 10 articles were published (out of 9 planned) across 7 online portals, achieving a total of 75,439 views.

2023: Two articles were published – one on a nationwide portal and one on a portal targeting local governments.

2024: Five articles were published. The key target groups and themes were identified based on the findings of the “*Analysis of the Most Promising LIFE Themes in Poland*” (T.2.1) and the experience of the Polish NCP. Three portals were selected: a construction-industry portal, a nationwide portal and a portal dedicated to environmental issues.

2025: Three articles were published. The campaign continued to build upon the results of the “*Analysis (...)*” (T.2.1) and the experience of the Polish NCP. Two nationwide portals and one portal aimed at local governments were selected for publication.

The campaign effectively raised awareness of the LIFE Programme and increased interest among potential beneficiaries.

To ensure long-term accessibility of the articles and to promote the results achieved within CBP, a dedicated webpage was created on the Polish NCP website: [Press Articles – LIFE NCP – National Fund for Environmental Protection and Water Management – Gov.pl](#).

The task was implemented in cooperation with the Media House contracted by NFOŚiGW in the respective year, under a framework agreement concluded in accordance with the Polish Public Procurement Law.

Overview of articles and statistics:

	year	article	portal	clicks
1	2023	"Program LIFE dla nauki i środowiska"	rp.pl	3 704

2	2023	"Program LIFE dla poprawy środowiska miast i gmin"	potralkomunalny.pl	b.d.*
3	2024	„Nowy Europejski Bauhaus w Programie LIFE – poznaj inicjatywę, która zmieni oblicze miast”	regiodom.pl	3 300
4	2024	„Program LIFE czeka na innowacyjne projekty środowiskowe i klimatyczne z obszaru close-to-market”	Wyborcza.biz	4 509
5	2024	„Projekty close-to-market w Programie LIFE, czyli biznes na rzecz klimatu i środowiska”	Teraz Środowisko	7 203
6	2024	„Nowy Europejski Bauhaus w Programie LIFE – kolejny nabór już w 2025 r.”		
7	2024	„Polska z sukcesem sięga po środki z Programu LIFE”		
8	2025	„Jak duży biznes korzysta z Programu LIFE?”	Wyborcza.biz	7 029
9	2025	„Te projekty służą respektowaniu przepisów środowiskowych. W Programie LIFE czekają duże pieniądze”	Portal Samorządowy	6 349
10	2025	„Pieniądze z Programu LIFE wspierają przejście na Czystą Energię”	portal WNP	43 345
SUMA:				75 439

*no data available due to technical limitations of the portal

**the articles were additionally distributed via newsletter to 25,000 subscribers

T.3.2 Conference – Financing Environmental Protection from EU Programmes (3 × 1) [Implemented, 100%]

Drawing on the network of contacts maintained by individual Polish National Contact Points for various EU-managed programmes, three online conferences entitled “Financing Environmental Protection from EU Programmes” were organised. The events focused on opportunities for financing activities related to environmental protection, nature conservation and climate action:

- [2023 Conference](#) (9 March 2023) – 424 participants
- [2024 Conference](#) (7 March 2024) – 464 participants
- [2025 Conference](#) (26 February 2025) – 909 participants

In total, 1,797 participants attended the conferences.

The conferences featured contributions from representatives of the NCPs of other EU programmes, who presented possibilities for implementing environmental and climate-related projects under: Horizon Europe, Innovation Fund, UrbAct, Interreg Europe, as well as the InvestEU financial instruments supporting environmental protection.

Recordings of the conferences (a total of 9 hours) are available on the NFOŚiGW YouTube channel, where they have gathered 1,850 views.

T.3.3 LIFE Information Days (3 × 2) [Implemented, 100%]

The LIFE Information Days were organised in a two-day format: one online day and one in-person day. The events were delivered in cooperation with external contractors selected in accordance with the Polish Public Procurement Law. Recordings of the events were produced and are available on the [NFOŚiGW YouTube channel](#)

Overall totals: 6 days of events / 764 in-person participants / 1,985 online participants / 2,586 YouTube views / 12 hours of material available on YouTube.

LIFE Information Days 2023

— 20 April 2023 – online (567 participants)

The event presented information on the 2023 LIFE Programme calls, partner-search opportunities for LIFE projects, and the role of Co-beneficiaries in national and international projects — an important opportunity for less experienced public and private entities seeking to participate in high-quality LIFE initiatives.

Speakers included, among others, a representative of the European Commission and Co-beneficiaries of ongoing LIFE projects.

The event recording is available as a training resource on the NFOŚiGW YouTube channel (545 views) – [link to recording](#).

— 11 January 2024 – in-person (312 in-person participants + 167 participants via YouTube streaming)

The event provided an introduction to the specific features of the LIFE Programme and showcased examples of Polish LIFE projects implemented in various sectors: business, research and local government. The results of 15 years of LIFE Programme implementation at NFOŚiGW were summarised, highlighting the contribution of LIFE projects to environmental and climate improvement in Poland. During the event, 20 awards in 13 categories were presented to the most active Polish LIFE Beneficiaries—a promotional activity supporting outreach and engagement among potential applicants.

The event recording is available on the YouTube channel (269 views) - [link to recording](#).

LIFE Information Days 2024

— 14 May 2024 – online (524 participants)

The event presented the scope of the new 2024 LIFE Programme calls, the role of the LIFE project monitoring team and the support provided by NFOŚiGW in implementing the LIFE Programme in Poland.

The event recording is available as a training resource on the NFOŚiGW YouTube channel (872 views) – [link to recording](#).

— **16 May 2024 – in-person (232 participants)**

Participants had the opportunity to familiarise themselves with LIFE projects showcased during thematic panels and at dedicated LIFE project stands. The event provided an opportunity for direct contact with current LIFE Beneficiaries, allowing participants to discuss and hear first-hand experiences of project implementation and its specific challenges.

The event also facilitated networking with potential partners for future LIFE projects.

In addition, a dedicated panel summarised 15 years of NFOŚiGW's involvement in LIFE and reviewed the results achieved through the implementation of the LIFE Programme in Poland.

The panel recording is available on the YouTube/LIFE channel (242 views) – [link to recording](#).

A report summarising the conference was also produced, serving both as an event summary and as promotional material for the LIFE Programme. It is available on the YouTube/LIFE channel (239 views) - [link to recording](#).

LIFE Information Days 2025

— **8 May 2025 – online (727 participants)**

Programme:

- New LIFE 2025 calls
- Overview of funding opportunities under other EU programmes
- Co-financing from NFOŚiGW and guidance on how to start developing a project
- Partnerships in LIFE projects

The event recording serves as a training resource and is available on the NFOŚiGW YouTube channel (419 views) – [link to recording](#).

— **13 May 2025 – in-person (220 participants)**

Programme:

- Summary of the 2024 LIFE Programme calls
- Presentations of 8 projects from the 2023 call that received EC funding in 2024
- 20 beneficiary stands, showcasing projects implemented with LIFE Programme funding
- 6 stands of National Contact Points (LIFE, InvestEU, Horizon Europe, URBACT) providing information on available EU funding opportunities
- Opportunity for valuable networking, exchange of experience, expanding cooperation and building partnerships

T.3.4 Series of information training sessions for staff of the European Funds Information Points (PIFE) (3 × 1) [Implemented, 100%]

Training sessions for the European Funds Information Points (PIFE) were organised annually, and a cooperation network was established with them to support the promotion of the LIFE Programme. The trainings were organised with the support of the Ministry of Funds and Regional Policy.

Totals: 329 online participants / 704 YouTube views / 2h16' of material available on YouTube.

21 and 23 March 2023 (153 participants)

The online training covered the fundamental aspects of the LIFE Programme, including a walkthrough of European Commission websites, the Funding & Tenders portal, and examples of LIFE projects.

The recording was made available to PIFE staff. **Additionally, to increase outreach, selected sections of the training were published on YouTube as Polish NCP training material:**

- [Where to Find Information on the LIFE Programme – CINEA / Funding & Tender Opportunities](#) (251 views)
- [The role of NFOŚiGW in implementing LIFE in Poland](#) (240 views)
- [Funded LIFE projects](#) (213 views)

6 March 2024 (47 participants)

The online training included: an update on the LIFE Programme and information on the 2024 call; examples of LIFE projects involving Polish entities; differences between the requirements of the LIFE Programme and selected other EU programmes; and practical guidance on how to support potential applicants.

The recording was made available to PIFE staff.

11 June 2025 (129 participants)

The online training covered: a short introduction to the LIFE Programme and the role of NFOŚiGW; new elements in the 2025 call; LIFE project databases and brokerage meetings organised by the European Commission; and Polish LIFE projects from the 2023 call.

The recording was made available to PIFE staff.

T.3.5 Online LIFE Programme Navigator [Implemented, 100%]

The concept of the Navigator was based on the extensive collection of recordings produced by the Polish NCP and published on the [NFOŚiGW YouTube](#) channel in the following sections: *LIFE 2021–2022*, *LIFE 2023–2024* and *LIFE 2025* — totalling almost 165 hours of recordings: CBP1 (2021–2022): 87 hours, and CBP2 (2023–2026): 78 hours.

These materials cover all aspects of the LIFE Programme: from introductory information, through updates on current calls, guidance on registration in the Funding & Tenders portal, the logic of LIFE projects, and examples of both Polish and international LIFE projects.

A concept was developed for a dedicated webpage that structures the Polish NCP's training materials available on the NFOŚiGW YouTube channel. Users are redirected from the webpage directly to specific segments of the relevant recordings.

The content of the webpage is organised into the following chapters:

- Introduction to the LIFE Programme
- Developing LIFE Projects
- Financial Sources for LIFE Projects
- Nature and Biodiversity Sub-programme (NAT)
- Circular Economy and Quality of Life Sub-programme (ENV)
- Climate Change Mitigation and Adaptation Sub-programme (CLIMA)
- Clean Energy Transition Sub-programme (CET)
- LIFE Programme for Business, Local Government and Research (C2M)

15 May 2024 - The Navigator was implemented in the form of a dedicated webpage: [YouTube LIFE PL Channel Navigator](#).

The webpage is systematically updated whenever new recordings are added to the NFOŚiGW YouTube channel.

T.3.6 Preparation of information and promotional materials [Implemented, 100%]

- **“Polish LIFE Projects”**

A printed publication and a PDF version compliant with WCAG requirements were prepared. This required collecting materials on all Polish LIFE projects, developing the content, followed by graphic design, layout of both book versions and printing.

The publication was produced in accordance with the Polish Public Procurement Law, requiring the conclusion of two contracts:

- for substantive development (September 2024 – February 2025),
- for graphic design, layout, WCAG compliant adaptation, printing and preparation of the PDF version (February 2025 – January 2026).

Implementation timeline:

collection of materials and substantive development of the publication: February 2025 – August 2025;

graphic design, layout, editing, book printing and PDF preparation (WCAG): August 2025 – January 2026

(during the layout stage, additional editing was required to shorten several project descriptions, which extended the implementation by two months).

The PDF version of the publication (WCAG-compliant) was published on 13 December 2025 on the [NCP LIFE in Poland](#) website.

The publication was promoted through NFOŚiGW and Polish NCP social media channels: Facebook: 3,182 views / LinkedIn: 660 views

Distribution of the publication:

The electronic version of the book was distributed by e-mail to:

- the database of potential LIFE applicants – developed as an outcome of the Analysis of the Most Promising LIFE Themes in Poland (T.2.1) (448 recipients);
- Polish LIFE Beneficiaries (237 recipients);

and via:

- the LIFE newsletter (4,843 recipients);
- the NFOŚiGW newsletter (2,948 recipients).



The printed version of the book (1,000 copies) was received from the contractor on 29 January 2026.


Distribution:

A total of 255 printed copies were sent to entities supporting the promotion of the LIFE Programme in Poland, including:

- Ministries that organise sectoral meetings for entrepreneurs and promote EU funds;
- Regional self-government units, to support the promotion of the LIFE Programme among local authorities;
- Forest administrations as well as national and landscape parks;
- Entities involved in environmental and water resource protection;
- National Contact Points of other EU programmes and funds;
- Journalists specialising in environmental topics.

The distribution plan for the printed book envisages using it as a tool to present the opportunities offered by the LIFE Programme — illustrated through completed projects — and as promotional material during:

- LIFE Information Days 2026 and 2027;
- meetings and events organised by the LIFE National Contact Point.

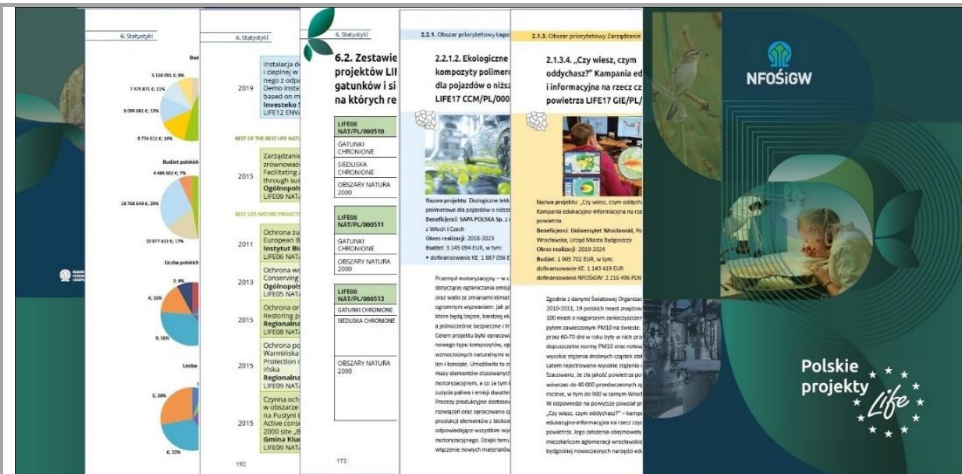

- Information brochures dedicated to individual sub-programmes / Infographics / Roll-ups

Brochures

A total of **4,000 copies** were printed.

Instead of producing four brochures of 1,000 copies each, dedicated to the individual LIFE sub-programmes, it was decided — with CINEA's approval (F&T portal, 25 August 2023) — to produce a single brochure providing an overview of the entire LIFE Programme. The brochure was developed internally (NFOŚiGW/LIFE). With CINEA's consent, elements of the leaflet *"The future is green. The future is LIFE"* — in particular iconography and layout — were used in the design (e-mail from CINEA-COMMUNICATION-LIFE dated 29 September 2023).

The information brochures were distributed continuously during events, promotional meetings, workshops and training sessions organised by the Polish NCP and by the NCPs of other EU programmes.

After completion of the CBP2 contract, a portion of the brochures remained available to the Polish NCP, and will continue to be used in ongoing promotional activities supporting the LIFE Programme in Poland.

A downloadable PDF version is available on the [NCP LIFE in Poland](#) website.



Infographics

CINEA granted permission to use the *infographics for LIFE sub-programmes* in brochures and roll-ups (e-mails from CINEA-COMMUNICATION-LIFE dated 5 September 2023 and 29 September 2023).



Roll-ups

Four roll-ups were produced, each dedicated to one of the LIFE sub-programmes (NAT, ENV, CLIMA, CET).

With CINEA's approval, the roll-ups were designed using LIFE iconography (e-mail from CINEA-COMMUNICATION-LIFE dated 5 September 2023).

The roll-ups are used in promotional activities during events, promotional meetings, workshops and training sessions organized by the Polish NCP and by the NCPs of other EU programmes.

Gadgets

Gadgets featuring the Polish NCP and LIFE Programme logos were produced by a contractor selected in accordance with the Polish Public Procurement Law in Q4 2023 and delivered in December 2023.

They were distributed continuously during LIFE Information Days, promotional events and meetings, workshops and training sessions organized by the Polish NCP and by the NCPs of other EU programmes.

After completion of the CBP2 contract, part of the gadgets remains available and will be used in future promotional activities supporting the LIFE Programme in Poland.

Types of gadgets (number produced) – stock remaining as of the project completion date:



- Laptop backpack-bag (70 produced) – black: 2, grey: 5, navy blue: 2
- Softshell jacket with hood (30 produced) – M: 6, L: 2, XL: 3
- Wireless headphones (100 produced) – 4
- Thermal mug with temperature indicator (200 produced) – black: 5, white: 2
- Waterproof *Dryinside* bag (300 produced):
 - Small – light grey: 0, dark grey: 0
 - Medium – navy: 10, green: 1, orange: 18
- Umbrella (200 produced) – black: 8, grey: 21, navy blue: 17
- Metal pen (2,000 produced) – navy blue: 291, green: 325

Other issues

Mention and explain unexpected events and adjustments that had to be made. Explain impact on other tasks, available resources and planning/timing. In case of major deviations from the planned budget, please refer to section 4.3.

T.3.1 b) During the contract negotiations with the European Commission, and following an analysis of the effectiveness of different media channels in reaching the target audience, the promotional approach for the LIFE Programme was changed from radio broadcasts to advertisements placed on specialized industry portals.

T.3.3 In 2023, with CINEA's approval and due to the contractor-selection procedure for NFOŚiGW events, as well as the parliamentary elections in Poland (which shifted public attention to other topics), the second day of the LIFE Information Day (the in-person component) was postponed to the second half of 2023. Ultimately, it took place in January 2024.

T.3.5 With CINEA's approval, the concept of the task was modified: instead of developing a navigator of LIFE-related websites, it was redesigned into a *Navigator of the extensive collection of films* produced by the Polish NCP and available on the YouTube channel.

T.3.6 a) Following a revision of the concept at a certain stage of project implementation, the task was delivered in its originally intended form: printing 1,000 copies of the publication and preparing a WCAG-compliant PDF version, which was published on the Polish NCP website.

	T.3.6 b) Brochures - The task was modified with CINEA's approval. Instead of producing four brochures, each dedicated to one LIFE sub-programme (1,000 copies each), a single brochure covering the entire LIFE Programme was prepared. T.3.6 b) Infographics - No new infographics were produced. Instead, the existing LIFE infographics developed by CINEA were used.
Milestones and deliverables (outputs/outcomes)	
See Technical Report (Part A).	

Work Package 4

Work Package 4: Find your partner for LIFE
Activities <i>Explain the work carried out for each work package during the reporting period, giving details of the work carried out by each participant involved. Please summarise in a few sentences what was done in the previous period, when applicable.</i> <i>Explain the reasons for <u>deviations</u> from Annex 1 of the Grant Agreement, the consequences and the proposed corrective actions.</i> <i>Include explanations for tasks not fully implemented, critical objectives not fully achieved and/or not being on schedule. Explain also the impact on other tasks, on the available resources and the planning. Where necessary, make reference to the deliverables in the report text. In case of major deviations from on the planned budget, please refer to section 4.3.</i> <i>Focus only on the main results as well as important lessons learned. The technical details should be provided in the deliverables.</i> <i>Additionally, for Operating Grants, report under Work Package 1 on <u>changes</u> in your organisation's capacity (if any) to become a more efficient stakeholder in the EU's policy process. Report on the proposed actions and their status to develop the organisation, widen the grassroots or members base, diversify and sustain the organisation's fundraising strategy and the strategy to reduce your dependence on LIFE operating grants.</i>
T.4.1 Creation of the database of potential applicants [Implemented, 100%] Based on the study “<i>Analysis of the Most Promising LIFE Themes in Poland</i>” (T.2.1), a list of entities identified as having the highest potential to apply for LIFE Programme funding was developed. This list constitutes the Database of Potential LIFE Applicants (D.4.1) and includes 448 entities. The database partially overlaps with entities with which the Polish NCP has already been in contact during its ongoing activities. In view of the added value of re-establishing contact and considering staff turnover, all entities in the database were contacted by e-mail to

present the LIFE Programme offer and the possibility of cooperation with the Polish NCP in the areas of application support and partner search for potential LIFE projects.

For specific groups of entities identified as having the highest potential to prepare LIFE projects within the Database of Potential Applicants (D.4.1), the following actions were undertaken:

- In 2024, information was distributed about:
 - the LIFE Programme, including a reference to the LIFE PL YouTube Navigator (T.3.5) and an attachment in the form of the information brochure (T.3.6);
 - opportunities for cooperation with the Polish NCP regarding project preparation support and partner search;
 - topics from the 2024 calls that could be of particular interest to a given entity (based on the findings of the Analysis – T.2.1).
- In 2025, information was distributed about:
 - the launch of the **LIFE 2025 calls**;
 - the possibility to consult LIFE project ideas online with the Polish NCP via [eKonsultantLIFE](#);
 - the publication of the series of 10 video podcasts “*Short on LIFE*” (T.2.4);
 - the online conference “*Financing Environmental Protection from EU Programmes*” (T.3.2);
 - the opportunity to participate in **brokerage meetings** (T.4.3);
 - invitations to LIFE training sessions and webinars (T.2.2);
 - the **LIFE Information Days** (T.3.3);

The possibility to download the digital version of the publication “*Polish LIFE Projects*” (T.3.6) from the [NCP LIFE in Poland](#) website.

T.4.2. Promotion of the Partner Search tools [Implemented, in a modified scope, 100%]

In 2024 and 2025, the Polish NCP carried out a verification of the cooperation offers available on the Funding & Tenders portal under the **Partner search announcements** section for each published call.

The verification showed that the overwhelming majority of offers were submitted not by entities preparing LIFE applications, but by organizations seeking to join a LIFE project, even when the **Expertise request** filter was applied.

Five offers were identified that could potentially constitute invitations to participate in specific projects; however, the descriptions provided were too general to enable implementation of step (a) under T.4.2, point 1, i.e. assessing the potential of these offers (initial evaluation of the project scope).

Nevertheless, due to the innovative nature of the proposed ideas and their potential suitability for LIFE Programme projects, the above-mentioned offers were published on the Polish NCP website in the section [Find a project partner](#). Selected offers were also

disseminated via the Polish NCP Newsletter and addressed directly to selected Polish entities (T.4.1 – Database of Potential Applicants).


With CINEA's approval, the name of MS 11 was modified as follows:

- from: *Identifying and delivering 20 cooperation offers*
- to: *Publishing 20 cooperation offers*


MS 11 was achieved above the planned level: as of 31 January 2026, a total of **26 cooperation offers from foreign partners seeking Polish partners were published** in the dedicated section of the Polish NCP website: [Find a project partner](#). Promotion of these offers was also carried out through the [NCP LIFE na LinkedIn](#) profile.

Events organized by the Polish NCP (or events in which the NCP participated) were systematically expanded to include information about, and promotion of, the opportunities offered by the Partner Search tool.

(slides from the LIFE NCP Poland presentation)



Additionally, the [YouTube LIFE PL Channel Navigator](#) (T.3.5) – includes training material on how to search for partners for LIFE projects, including the use of the Partner Search tool.



With the European Commission's approval, the scope of the task was modified. In addition to the annual review of Partner Search offers, cooperation was established with a strategic entity responsible for the protection of aquatic ecosystems in Poland: State Water Management Polish Waters (PGW Wody Polskie).

The cooperation consists of developing project proposals in partnerships with interested stakeholders, in particular civil-society organisations and research institutions, within the framework of a dedicated Working Group, which meets several times a year. During the project implementation period, seven meetings of the Working Group were held.

The Group worked on:

- eight projects submitted in 2024 and rejected, with the intention of resubmission in 2025, and
- five new project concepts for the 2025 call.

As a result of the Working Group's activities, six proposals were submitted under the LIFE 2025 calls, with PGW Wody Polskie acting as the lead beneficiary in five of them and as a partner in one.

Further submissions are planned for the 2026 calls.

T.4.3. Promotion, Participation and Support for Applicants in Brokerage Meetings [Implemented, in a modified scope, 100%]

The Polish NCP promoted brokerage meetings – virtual 1:1 meetings – through a variety of channels:

- Website publications:
 - [Find a Project Partner](#) (2023)
 - [Support for Applicants in Brokerage Meetings Organised by the European Commission – Virtual 1:1 Meetings](#) (2024)
- Newsletter Polish NC LIFE
- LinkedIn posts published via the [Polish NCP LIFE profile](#)

d) During events organized by or attended by the Polish NCP.

The image shows two screenshots. The left screenshot is from the 'Krajowy Punkt Kontaktowy LIFE' website, displaying information about virtual meetings and a list of participants. The right screenshot is from the '#EULIFE25 INFO DAYS' virtual meetings interface, showing a 'Networking' section with instructions on how to request a meeting and a list of potential partners.

Krajowy Punkt Kontaktowy LIFE
172 obserwujących
172 obserwujących

Zobacz kolekcję aktywnych lub wcześniejszych reklam Krajowy Punkt Kontaktowy LIFE.
Wyświetl bibliotekę reklam

Wszystkie Zdjęcia Wideo Artykuły Dokumenty
Sortuj wg: Najpopularniejsze

Krajowy Punkt Kontaktowy LIFE
172 obserwujących
13 min •

Wspieracie dla Wnioskodawców LIFE dzięki Virtual Meetings 111!

Virtual meetings 1:1 to ciekawa inicjatywa Komisji Europejskiej, która umożliwia spotkania on-line z podmiotami, które poszukują partnerów do projektu LIFE.

W tegorocznym naborze, spotkania brokerskie będą prowadzone do 30 września 2024 r. To doskonała okazja do nawiązania kontaktów i znalezienia potencjalnych partnerów do współpracy.

Więcej informacji na temat spotkań brokerskich: <https://lnkd.in/d/vlavMcA>

Oferujemy wsparcie w przygotowaniach do udziału w spotkaniach:
• wstępna ocena koncepcji projektu LIFE - zapraszamy do skorzystania z narzędzia eKonsultantLIFE (<https://lnkd.in/d/mj2KkN>)
• wsparcie w określeniu potencjalnych partnerów do projektu LIFE z bazy uczestników spotkań brokerskich – prosimy o kontakt za pośrednictwem lfe@infosig.gov.pl

#LIFEProgramme #Networking #Innovation #EUProjects #VirtualMeetings #NFOSIGW

#EULIFE24 INFO DAYS
23 - 26 APRIL 2024

Home Agenda Networking My schedule Virtual meetings Profile
Sign out

Networking

This page shows the people attending this event. Click on the "request meeting" button to set up a meeting with someone. You can filter the participants through the fields below, and their areas of activity.

Networking opportunities in the format of 1:1 bilateral virtual meetings among potential applicants and with representatives of National Contact Points (NCPs) are available during the period from 13 May to 30 September 2025.

- You can identify them below and select them based on their areas of activity.
- Please, indicate the area and subject of your proposal in the meeting request.
- Meeting requests have to be approved to be scheduled.

A number of representatives of National Contact Points (NCPs) will also be available for bilateral virtual meetings with potential applicants.

Virtual meetings: EU Life Info Days 2025

Looking for a partner?
Your LIFE project could be more successful if you collaborate with like-minded partners. You can find potential partners through:

- 1-to-1 meetings with other applicants on the [networking platform](#) launched during the EU LIFE Info Days
- [Funding & tender opportunities portal](#)
- [Enterprise Europe Network](#)
- Your nearest [National Contact Point \(NCP\)](#)

On the CINEA platforms launched annually as part of the LIFE Info Days, the list of registered Polish NCP staff members is visible, confirming their availability for participation in brokerage meetings in 2023, 2024 and 2025 (2–4 staff members each year).

To the date of submission of this report, the Polish NCP has not received any offers or enquiries through the platform.

With the approval of CINEA, the scope of Task T.4.3 was extended to include consultation meetings with potential LIFE applicants, and the target indicators were revised as follows:

- Changed from: Participation in approx. 10 (individual) brokerage meetings per year
- Changed to: Participation in approx. 25 (individual) brokerage/consultation meetings per year

These revised targets were exceeded. During the reporting period (February 2023 – January 2026), staff of the Polish NCP LIFE took part in over 120 meetings with potential LIFE applicants (2023: 25 meetings, 2024: 54 meetings, 2025: 48 meetings, 2026: 1 meeting). During these meetings, project ideas were discussed, including considerations related to potential consortium composition.

Other issues

Mention and explain unexpected events and adjustments that had to be made. Explain impact on other tasks, available resources and planning/timing.

T.4.2 With the approval of CINEA, the name of MS 11 was modified as follows:

- Changed from: *Identifying and delivering 20 cooperation offers*
- Changed to: *Publishing 20 cooperation offers*

Additionally, the deadline for its achievement was adjusted from 30/04/2024 to 31/01/2026.

In case of major deviations from the planned budget, please refer to section 4.3.

T.4.3 With the approval of CINEA, the scope of the task was extended to include consultation meetings with potential LIFE applicants, and the target indicators were revised as follows:

- Changed from: Participation in approx. 10 (individual) brokerage meetings per year
- Changed to: Participation in approx. 25 (individual) brokerage/consultation meetings per year.

Milestones and deliverables (outputs/outcomes)

See Technical Report (Part A).

Timetable

ACTIVITY	YEAR 1				YEAR 2				YEAR 3			
	Q 1	Q 2	Q 3	Q 4	Q 1	Q 2	Q 3	Q 4	Q 1	Q 2	Q 3	Q 4
Task 1.1 - Formation of the project team												
Task 1.2 - Project management and monitoring												
Task 1.3 - Effects monitoring												
Task 2.1 - Analysis of the most promising LIFE topics in Poland												
Task 2.2 - Thematic trainings for applicants												
Task 2.3 - Practical workshops for specialists on the preparation of applications												

Task 2.4 - Podcast series on key aspects of project preparation												
Task 2.5 - Training and support for NCP staff												
Task 3.1 - Media activities												
Task 3.2 - Conference "Financing environmental protection from EU Programmes"												
Tast 3.3 - LIFE Info Days												
Task 3.4 - A series of information trainings for employees of European Funds Information Points Informacyjnych Funduszy Europejskich												
Task 3.5 - Online guide (navigator) to LIFE topics and requirements												
Task 3.6 - Preparation of information and promotional materials												
Task 4.1 - Database of potential applicants												
Task 4.2 - Promotion of Partner Search tools												
Task 4.3 - Promotion, participation and support for applicants in brokerage meetings												

#@PRJ-MGT-PM@#

3.2 Impact monitoring and reporting

Impact monitoring, evaluation and reporting strategy

Report on changes to the impact monitoring and evaluation strategy (if any)

There were no changes to the impact monitoring and evaluation strategy.

#\$PRJ-MGT-PM\$# #@COM-DIS-VIS-CDV@#

3.3 Communication, dissemination and visibility

Communication, dissemination and visibility of funding

Report on the communication and dissemination activities undertaken (to whom, which format, how many, etc.).

Describe how the visibility of EU funding was ensured.

If you described your project on your website(s) and/or social media accounts, please provide the links.

Report on any important changes to your dissemination and communication strategy.

The communication and dissemination activities carried out under the project aimed to increase interest in the LIFE Programme among key target groups. They were implemented in cooperation with a Media House selected in accordance with Polish Public Procurement Law, and through the use of media and information channels directed at defined audiences, including: trade media, nationwide media and social media.

The activities were conducted throughout the entire project implementation period, with particular emphasis on the periods of calls for proposals to the LIFE Programme announced by the European Commission / CINEA.

Communication and dissemination activities were directed at all entities that could potentially apply to the LIFE Programme, with **particular attention given to groups identified as having the highest potential to prepare projects in the ENV, CLIMA and CET areas:**

- **Entrepreneurs, in particular medium-sized enterprises with production or service profiles**

Examples of communication and dissemination activities:

- Webinar (T.2.2): *LIFE in Business – Close2Market (C2M)* with the participation of representatives of the European Commission (2023)
- Advertisements (T.3.1): published on the following portals: *Money.pl*, *Egospodarka.pl*, *Business Insider*
- Articles (T.3.1):
 - “Close-to-market projects in the LIFE Programme – business for climate and the environment” (2024)
 - “The LIFE Programme is looking for innovative environmental and climate projects in the close-to-market area” (2024)
 - “How do large companies benefit from the LIFE Programme?” (2025)
- Promotional film (T.3.1): *LIFE – Circular Economy and Quality of Life* – illustrated through the example of a project implemented by a commercial company (2025)
- Podcast (T.2.4): *Close to Market (C2M) Projects* (2025)
- Dedicated section in the Navigator (T.3.5): *The LIFE Programme for business, local authorities and science (C2M)*
- Participation of a Polish NCP representative in events addressed to entrepreneurs:
 - Conference: “Grants for innovation for your company. National and international support sources.” (2023)
 - *European SME Congress* (2024)

- *Horizon4Poland'24* (2024)
- Conference: *"Grants, Innovation, Sustainable Development – opportunities for companies"* (2025)
- *CLIMATE-CON Conference* (2025)
- **Research and scientific institutions, in particular those whose activities relate to environmental and climate issues.**
Examples of communication and dissemination activities:
 - Article (T.3.1): *"The LIFE Programme for Science and the Environment"* (2023)
 - Advertisements (T.3.1): published on the following portals: *Money.pl*, *Egospodarka.pl*, *Business Insider*
 - Promotional film (T.3.1): *LIFE – Climate Change Mitigation and Adaptation* – based on the example of a project implemented by a research institution (2025)
 - Dedicated section in the Navigator (T.3.5): *The LIFE Programme for business, local authorities and science (C2M)*
 - Participation of a Polish NCP representative in events addressed to research and scientific institutions:
 - Conference *"3rd Edition of the Łukasiewicz Innovatorium"* (2023)
 - NCBR Conference *"Circular Bioeconomy – Funding for Research and Innovation"* (2023)
 - *Second Meeting of the Users of the Copernicus Atmosphere Monitoring Service*, organised by IOŚ-PIB (2024)
- **Local authorities at various levels, in particular those with the greatest potential to coordinate projects: large city and regional authorities.**
Examples of communication and dissemination activities:
 - Articles (T.3.1):
 - *"The LIFE Programme for Improving the Environment of Cities and Municipalities"* (2023)
 - *"The New European Bauhaus in the LIFE Programme – discover the initiative that will reshape cities"* (2024)
 - *"The New European Bauhaus in the LIFE Programme – next call already in 2025"*
 - Dedicated section in the Navigator (T.3.5): *The LIFE Programme for business, local authorities and science (C2M)*
 - Participation of a Polish NCP representative in events targeting local authorities:
 - *Marshal's Assembly (Konwent Marszałków)* (2023 / 2024 / 2025)
 - *"Partnerska Inicjatywa Miast ALUMNI" Conferences* (2023 / 2024 / 2025)
 - *UrbAct Info Days webinars* (2023 / 2024 / 2025)
 - Webinar *"The LIFE Programme for Local Government Units (JST)"* (2025)
 - Promotional film (T.3.1): *LIFE – Climate Change Mitigation and Adaptation* – illustrated through the example of a project implemented by a local government unit (2025)
- **Industry organisations, associations and foundations.**
Examples of communication and dissemination activities:
 - Participation of a Polish NCP representative in events addressed to industry organisations, associations and foundations:
 - *Galvanisers' Conference* (2024)
 - Webinar *"Energy efficiency – financial support for SMEs"* (2024)
 - Meeting with NGOs at the NFOŚiGW headquarters (2025)
 - *Convention of Ambassadors of EU Funds* (2025)

Further communication and dissemination activities were directed in particular to groups identified as having the highest potential to prepare LIFE project proposals within the **Database of Potential Applicants** (D.4.1), including:

- Distribution in 2024 of information on:
 - the LIFE Programme, with reference to the Navigator (T.3.5) and an attached information brochure (T.3.6)
 - the possibility of cooperation with the Polish NCP in the area of project preparation support and partner search
 - 2024 call topics that could be of interest to specific entities (based on findings from the Analysis under T.2.1)
- Distribution in 2025 of information on:
 - the launch of the LIFE 2025 calls
 - the possibility of online consultation on LIFE project ideas with the Polish NCP (*eKonsultantLIFE*)
 - the publication of the series of ten video podcasts “*LIFE: Short overview*” (T.2.4)
 - the online conference “*Financing Environmental Protection from EU Programmes*” (T.3.2)
 - the possibility of participating in brokerage meetings (T.4.3)
 - invitations to LIFE training sessions and webinars (T.2.2)
 - LIFE Information Days (T.3.3)
 - the option to download from the Polish NCP LIFE in Poland website the digital version of the publication “*Polish LIFE Projects*” (T.3.6)

Communication activities undertaken:

- 49 presentations on the scope of the LIFE Programme and the offer of the Polish NCP delivered at external events (2023 / 2024 / 2025)
- 89 editions of the Polish NCP Newsletter (2023, 2024, 2025) – 4,843 subscribers
- 137 news items published on the Polish NCP website (2023, 2024, 2025)
- 96 LinkedIn posts (2024, 2025)

Dissemination activities undertaken:

- Implementation of 31 information or training events, attended by 6,065 participants (compared to approx. 2,300 planned for the entire duration of the project), including:
 - 4 online workshops on preparing applications for individual LIFE sub-programmes (2023), with recordings available on the NFOŚiGW YouTube channel (a total of 179 participants and 1,654 YouTube views)
 - 6 in-person practical workshops on preparing LIFE applications (2024 and 2025) (a total of 87 participants)
 - 9 thematic training sessions for applicants (2023–2025), with recordings available on the NFOŚiGW YouTube channel (a total of 924 participants and 1,187 YouTube views)
 - 3 conferences under the theme *Financing Environmental Protection from EU Programmes* (2023, 2024, 2025), with recordings available on the NFOŚiGW YouTube channel (1,797 participants / 1,850 YouTube views)
 - 3 × 2 LIFE Information Days (2023, 2024, 2025), with recordings available on the NFOŚiGW YouTube channel (544 participants on-site / 1,985 online participants / 2,347 YouTube views)
 - 3 online training sessions for the EU Funds Information Points (2023, 2024, 2025) – 329 participants

- Publication of 10 articles across 7 online portals, which collectively generated 75,439 views, including:
 - 2023 – 2 articles published on one nationwide and one local-government-focused portal
 - 2024 – 5 articles, with key audiences and topics identified on the basis of findings from “*Analysis of the most promising LIFE themes in Poland*” (T.2.1) and Polish NCP experience; published on three portals: one construction-sector portal, one nationwide portal, and one environmental portal
 - 2025 – 3 articles, continuing the campaign based on T.2.1 findings and NCP experience; published on two nationwide portals and one local-government portalAll articles were also published on the Polish NCP website.

Implementation of 3 advertising campaigns (2023, 2024, 2025), promoting the LIFE Programme and the Polish NCP through banner advertisements on selected nationwide and sectoral websites, redirecting to the [NCP LIFE in Poland](#) website.

These campaigns generated a total of 3,205,360 ad impressions and 18,185 clicks.

Communication and dissemination activities were carried out using the visual identity developed under the project (T.3.1) together with the LIFE logo. This applied both to external publications and materials, as well as to materials prepared for the purposes of trainings, presentations and conferences. **Information (brochure) and promotional materials (roll-ups, gadgets, backdrops) produced under activity T.3.6 were used on an ongoing basis.**

EXAMPLES:



Roll-ups (T.3.6)

– each dedicated to one of the four LIFE sub-programmes (NAT, ENV, CLIMA, CET)

— Information brochure (T.3.6)



— Backdrops (T.3.6)

— Articles (T.3.1) – e.g. the article “Funds from the LIFE Programme support the transition to Clean Energy” published on the *wnp.pl* portal (2025)

Pieniądze z Programu LIFE wspierają przejście na Czystą Energię

Program LIFE to jedyny instrument finansowy Unii Europejskiej poświęcony wyłącznie współfinansowaniu projektów z dziedziny ochrony środowiska, w tym przyrody oraz ograniczenia wpływu człowieka na klimat i dostosowania się do jego zmian. Jego głównym celem jest wspieranie procesów wdrażania wspólnotowego prawa ochrony środowiska, realizacja unijnej polityki w tym zakresie, a także identyfikacja i promocja nowych rozwiązań dla problemów dotyczących środowiska i klimatu.


Autor: Płatna współpraca z Narodowym Funduszem Ochrony Środowiska i Gospodarki Wodnej
Dodano: 27 sierpnia 2025 16:30

Podziel się



Poglądy i wyrażone opinie są wyłącznie poglądami autora (autorów) i niekoniecznie odzwierciedlają poglądy Unii Europejskiej lub CINEA. Zarówno Unia Europejska, jak i organ przyznający dofinansowanie - nie ponoszą za nie odpowiedzialności.

— Advertisements (T.3.1) – graphics published on websites in 2023, 2024 and 2025






— Presentations – closing slide



— Information materials – DI LIFE (T.3.3) graphics used for event promotion on social media (2024, 2025)



Films – examples:



- | | | |
|---|--|---|
| 1 | | LIFE - Łagodzenie zmian klimatu i przystosowanie się do nich, na...
Narodowy Fundusz Ochrony Środo... |
| 2 | | LIFE Łagodzenie zmiany klimatu i przystosowanie się do niej
Narodowy Fundusz Ochrony Środo... |
| 3 | | LIFE Przejście na czystą energię – na przykładzie projektu...
Narodowy Fundusz Ochrony Środo... |
| 4 | | LIFE Gospodarka o obiegu zamkniętym i jakość życia.
Narodowy Fundusz Ochrony Środo... |
| 5 | | Przyroda i różnorodność biologiczna – na przykładzie...
Narodowy Fundusz Ochrony Środo... |


Graphics promoting the films – examples:



Podcasts – examples:



— Promotion of podcasts on the website and social media – example:

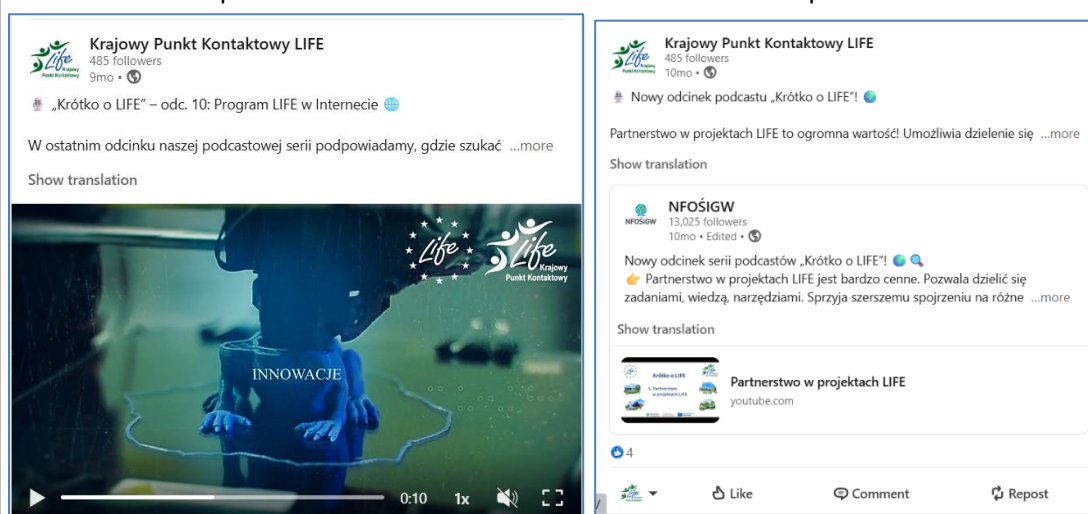

Monitoring of promotional activities was carried out through media monitoring for mentions of the keyword “LIFE”. Monthly summaries were prepared indicating the number of references to the LIFE Programme available in the media.

Polish NCP described Capacity Building Project (CBP 4 LIFE_PL):

- on it's website: [Project 101101078 — LIFE21-CAP-PL-CBP 4 LIFE_PL](#)
- on LinkedIn: [Krajowy Punkt Kontaktowy LIFE: Omówienie | LinkedIn](#)

#SCOM-DIS-VIS-CDV\$# #CON-SOR-CS@#

4. RESOURCES

4.1 Consortium set-up

Consortium cooperation and division of roles (if applicable)

Report on changes in the consortium composition (including structural, legal or management changes, if any) or its key personnel.

For Operating Grants: Report only on changes to key personnel.

The project was implemented independently by NFOŚiGW.

Changes in the involvement of key personnel were presented in the description of activity T.1.1.

#CON-SOR-CS\$# #PRJ-MGT-PM@#

4.2 Project management

Project management, quality assurance and monitoring of progress

Report on changes to the overall project management approach (including quality assurance and monitoring).

Report on important changes in the way the consortium is managed, participants work together (Beneficiaries, Affiliated Entities, Associated Partners, etc.) and interact with key stakeholders, and decisions are taken. (n/a for Operating Grants)

For SIPs/SNAPS: In addition, briefly report on how you manage the interaction with the complementary actions and the public and private funds secured, as well as on how you involve key stakeholders. Highlight any important problem encountered.

Project management was conducted smoothly.

Continuity of management was affected by a change in the position of Project Manager between 1 September 2023 and 12 April 2024. However, this change was short-lived, and

from 13 April 2024 until the end of the project, coordination was carried out by a person involved in the implementation of the LIFE Programme in Poland since 2008, with team management experience dating back to 2004.

The project was coordinated in line with the established assumptions and exceeded the planned results.

#\$PRJ-MGT-PM\$# #@\$FIN-MGT-FM@\$#

4.3 Budget

Budget implementation — Use of resources (deviations) (n/a for Lump Sum Grants) (n/a for Additional Prefinancing Report)

Explain major deviations from the budget planning (i.e. differences between actual and planned use of resources, especially for personnel).

Include explanations on major budget transfers between cost categories in the estimated budget (if applicable). Explain unforeseen subcontracting in the 'Report on the Use of Resources', not here. If needed, add explanations linked to the report on the use of resources filled in online. Ensure consistency with that report.

Deviations from the budget planning are presented in the table:

CATEGORY	GRANT AGREEMENT	ACTUAL COSTS
Personnel cost	306 499,00 EUR	307 086,36 EUR
Subcontracting	43 938,00 EUR	33 794,30 EUR
Other direct cost	179 103,00 EUR	181 897,50 EUR
TOTAL:	529 540,00 EUR	522 778,16 EUR

Explanations of major deviations from the budget planning and major budget transfers between cost categories in the estimated budget:

1. The personnel cost was a little higher than it was planned (+587,36 EUR).
2. Subcontracting cost were lower, than it was planned (-10 143,70 EUR), because of:
 - a. lower costs of preparation of a visual identification system (T.3.1) and publication "Polish LIFE projects" (T.3.6)
 - b. changing the scope of T.21 (details in the task description)
3. Other direct cost were higher, than it was planned (+2 794,50 EUR) mainly because underestimated costs of audio-visual materials (T.2.2), which were reported in midterm report.

Unforeseen subcontracting – none.

Extra explanations linked to the report on the use of resources filled in online – none.

Other issues	none
--------------	------

#\$FIN-MGT-FM\$# #@\$RSK-MGT-RM@\$#

4.4 Risk management

Critical risks and risk management strategy

Report on the state of play concerning the risks and risk mitigation measures (if any).

Throughout the entire project, risk was managed in accordance with the adopted assumptions.

Some risks did materialize, for example prolonged procurement procedures. However, all planned activities—taking into account the modifications agreed with CINEA—were successfully completed within the project implementation period.

See Technical Report (Part A).

#§RSK-MGT-RM§#

4.5 Next phase: Changes/adjustments

Next phase: changes/adjustments *(for SIPs/SNAPs; n/a for Final Report)*

Confirm that the planning for the next phase/reporting period remains as foreseen in Annex 1 of the Grant Agreement or, if necessary, present additional details on the work plan, highlighting in particular, for each activity/task, technical, financial or timetable deviations.

Mention the main targets and goals for next phase, unless already clear in Annex 1 of the Grant Agreement.

Additionally, if deviations are anticipated, please:

- copy an updated table of deliverables and milestones into section 1.2, highlighting the changes (and any deletions)
- update the timetable in section 1.3.

Note: If the details for the next phase imply a substantial change to Annex 1 of the Grant Agreement (e.g. non-minor technical, administrative, and financial changes), you must request a formal amendment. You can however already mention them in this report, if agreed with the granting authority and the external monitoring team. In this case, please briefly mention the agreement here.

Insert text

#@FOL-UP-FU@#

5. FOLLOW-UP TO EU RECOMMENDATIONS

5.1 Follow-up to EU recommendations

Follow-up to EU recommendations .

Highlight corrective actions taken as a result of EU monitoring activities (including follow-up to EU project reviews or feedback on previous periodic reports, if any). List each recommendation/comment and explain how they have been followed up.

The recommendations received February 15th, 2024 from Elisabetta Scialanca, Project Adviser, CINEA, after Project Monitor visit November 15th, 2023 were taken into account in the further implementation of the project.

(...)

#§FOL-UP-FU§# #@ETH-ICS-EI@#

6. OTHER

6.1 Ethics

Ethics

Not applicable.

#§ETH-ICS-EI§# #@SEC-URI-SU@#

6.2 Security

Security

Not applicable.

#§SEC-URI-SU§# #@DEC-LAR-DL@#

7. DECLARATIONS

[OPTION 1 by default (all except OG):

Double funding	
Information concerning other EU grants for this project  Please note that there is a strict prohibition of double funding from the EU budget (except under EU Synergies actions).	YES/NO
We confirm that to our best knowledge neither the project as a whole nor any parts of it benefit/have benefitted from any other EU grant (including EU funding managed by authorities in EU Member States or other funding bodies (e.g. U Regional Funds, EU Agricultural Funds, etc)). If NO, explain and provide details	YES
We confirm that to our best knowledge neither the project as a whole nor any parts of it are (nor will be) submitted for any other EU grant (including EU funding managed by authorities in EU Member States or other funding bodies (e.g. EU Regional Funds, EU Agricultural Funds, etc)). If NO, explain and provide details.	YES

#\$DEC-LAR-DL\$#

]

[OPTION 2 for Operating Grants:

Rate of use for the action <i>(n/a for Additional Prefinancing Report)</i> Declare if there were any <u>changes</u> to the rate of use for the action (i.e. the percentage of your organisation's activities which is eligible under this grant, meaning the percentage of activities that comply with the policy objectives of the call, is inside the geographic area of eligibility, etc as compared to the percentage of activities that are ineligible).	
Rate of use for the action:	<u>insert rate</u> %

Double funding	
Information concerning other EU operating grants  Please note that there is a strict prohibition of double funding from the EU budget (except under EU Synergies actions).	YES/NO
We confirm that to our best knowledge we do not benefit/have not benefitted from any other EU operating grant for the same period. If NO, explain and provide details.	YES
We confirm that we have not requested any other EU operating grant for the same period. If NO, explain and provide details.	YES

#\$DEC-LAR-DL\$#

]

HISTORY OF CHANGES		
VERSION	PUBLICATION DATE	CHANGE
1.0	01.04.2022	Initial version (new MFF).
2.0	01.12.2024	Small corrections in the instructions in sections 2.2 and 3.1.
